For RAVENNA ARMY AMMUNITION PLANT

FY04 as of January 2004




Table of Contents

| | ntents | |
|-----------------|--|---|
| Purpose | | |
| | | |
| - | Abbreviations | |
| Approval | | 6 |
| SUMMARY | | |
| Installation A | Action Plan Summary | 1 |
| INSTALLAT | ION INFORMATION & DESCRIPTION | |
| Installation Ir | nformation | 1 |
| Installation D | Description | 2 |
| CONTAMINA | ATION ASSESSMENT | |
| Contamination | on Assessment | 1 |
| Previous Stu | udies | 3 |
| SITE DESCI | RIPTIONS | |
| | A Eligible Sites | 1 |
| RVAAP-01 | Ramsdell Quarry Landfill | |
| RVAAP-02 | Erie Burning Grounds | |
| RVAAP-04 | Open Demolition Area #2 | |
| RVAAP-05 | Winklepeck Burning Grounds | |
| RVAAP-06 | C Block Quarry | |
| RVAAP-08 | Load Line 1 | |
| RVAAP-09 | Load Line 2 | |
| RVAAP-10 | Load Line 3 | |
| RVAAP-11 | Load Line 4 | |
| RVAAP-12 | Load Line 12 Dilution/Settling Pond | |
| RVAAP-13 | Bldg. 1200-Dilution/Settling Pond | |
| RVAAP-16 | Fuze and Booster Quarry Landfill/ Pond | |
| RVAAP-19 | Landfill North of Winklepeck Burning Grounds | |
| RVAAP-28 | Mustard Agent Burial Site | |
| RVAAP-29 | Upper & Lower Cobb Ponds | |
| RVAAP-32 | 40 & 60 MM Firing Range | |
| RVAAP-33 | Load Line 6 | |
| RVAAP-34 | Sand Creek Disposal Road Landfill | |
| RVAAP-36 | Pistol Range | |
| RVAAP-38 | NACA Test Area | |
| RVAAP-39 | Load Line 5 | |
| RVAAP-40 | Load Line 7 | |
| RVAAP-41 | Load Line 8 | |
| RVAAP-42 | Load Line 9 | |
| RVAAP-43 | Load Line 10 | |
| RVAAP-44 | Load Line 11 | |
| RVAAP-45 | Wet Storage Area | |
| RVAAP-46 | Bldg F-15 & F-16 | |
| RVAAP-48 | Anchor Test Area | |
| RVAAP-49 | Central Burn Pits | |
| RVAAP-50 | Atlas Scrap Yard | |
| · · | , | _ |

Table of Contents

| RVAAP-51 | Dump Along Paris-Windham Road | 33 |
|---------------|--|------------|
| Response C | omplete Sites | 34 |
| RVAAP-03 | Open Demolition Area #1 | |
| RVAAP-07 | . Bldg. 1601 Hazardous Waste Storage | |
| RVAAP-14 | Load Line 6 Evaporation Unit | |
| RVAAP-15 | Load Line 6 Treatment Plant | |
| RVAAP-17 | Deactivation Furnace | 37 |
| RVAAP-18 | Load Line 12 Wastewater Treatment Plant | 37 |
| RVAAP-20 | Sand Creek Sewage Treatment Plant | 38 |
| RVAAP-21 | Depot Sewage Treatment Plant | |
| RVAAP-22 | George Road Sewage Treatment Plant | |
| RVAAP-23 | Unit Training Equipment Site UST | 39 |
| RVAAP-24 | Waste Oil Tank | 40 |
| RVAAP-25 | Bldg. 1034 Motor Pool AST | 40 |
| RVAAP-26 | Fuze Booster Area Settling Tanks | 41 |
| RVAAP-27 | Building 854, PCB Storage | 41 |
| RVAAP-30 | Load Line 7 Wastewater Treatment | <i>4</i> 2 |
| RVAAP-31 | Ore Pile Retention Pond | <i>4</i> 2 |
| RVAAP-35 | 1037 Building - Laundry Wastewater Sump | <i>4</i> 3 |
| RVAAP-37 | Pesticide Building S-4452 | |
| RVAAP-47 | Building T-5301 | 44 |
| SCHEDULE | | |
| Past Mileston | nes | 1 |
| | lestones | |
| • | ction Sites | |
| Schedule Ch | art | 3 |
| | | |
| | ON ACTIVITIES CONTRACTOR OF THE STATE OF THE | |
| | al / Interim Remedial Action / Remedial Action Assessment | |
| | oval / Interim Remedial Action / Remedial Action Assessment | |
| Future Remo | oval / Interim Remedial Action / Remedial Action Assessment | 1 |
| COST ESTI | MATES | |
| Prior Year Fu | unds | 1 |
| Unconstraine | ed (Required) Cost-to-Complete | |
| | (Programmed) Cost-to-Complete Chart | |
| COMMINIT | Y INVOLVEMENT | |
| | Advisory Board Status | 1 |

Statement of Purpose

The purpose of the Installation Action Plan (IAP) is to outline the total multi-year restoration program for an installation. The plan will define Installation Restoration Program (IRP) requirements and propose a comprehensive approach and associated costs to conduct future investigations and remedial actions at each Area of Concern (AOC) at the installation.

In an effort to coordinate planning information between the IRP manager, major army commands (MACOMs), installations, executing agencies, regulatory agencies, and the public, an IAP has been completed for the Ravenna Army Ammunition Plant (RVAAP). The IAP is used to track requirements, schedules and tentative budgets for all major Army installation restoration programs.

All site-specific funding and schedule information has been prepared according to projected overall Army funding levels and is therefore subject to change during the document's annual review. Under current project funding, all remedies will be in place at the RVAAP by the end of FY 2014.

The following people contributed this the IAP.

Glen Beckham

Army Corp of Engineers, Louisville

Dr. David J. Brancato

Army Corp of Engineers, Louisville

Bonnie Buthker

Ohio Environmental Protection Agency

Ohio Environmental Protection Agency

Todd R. Fisher

Ohio Environmental Protection Agency

Tiffany Gates-Tull

Engineering & Environment for AEC

John Jent

Army Corp of Engineers, Louisville

Joe King Army Environmental Center

Timothy Lamb Army Corp of Engineers, Louisville

Eileen Mohr Ohio Environmental Protection Agency

Mark Patterson Ravenna Army Ammunition Plant

LTC Tom Tadsen Ohio Army National Guard

JoAnn Watson Army Environmental Center

Paul Zorko Army Corp of Engineers, Louisville

Acronyms & Abbreviations

Army Environmental Database - Restoration AEDB-R

AEHA (United States) Army Environmental Hygiene Agency

Area of Concern AOC bgs below ground surface

CERCLA Comprehensive Environmental Response Compensation and Liability Act (1980)

CERCLIS **CERCLA Inventory System**

CHPPM (United States Army) Center for Health Promotion and Preventive Medicine

COEC Consituent of Ecological Concern COPC Chemical of Potential Concern

DD**Decision Document**

DoD U.S. Department of Defense DOT Department of Transportation

Defense Site Environmental Restoration Tracking System (Now AEDB-R) **DSERTS**

EPA Environmental Protection Agency ERA Ecological Risk Assessment

Environmental Restoration, Army (formally called DERA) ER,A

Fixed Price Remediation with Insurance **FPRI**

FS Feasibility Study FY Fiscal Year

GOCO Government-Owned, Contractor-Operated octahydro-1,3,5,7-tetranitro-1,3,5,7-tetrazacine **HMX**

IAP Installation Action Plan IRA Interim Removal Action

Installation Restoration Program **IRP** LAP Load, Assemble and Pack

LL Load Line

LTM Long Term Monitoring **Major Command** MACOM

Maximum Contaminant Level MCL

Military Munitions Response Program MMRP National Advisory Committee on Aeronautics NACA

NCP National Oil and Hazardous Substances Pollution Contingency Plan

NE Not Evaluated

National Environmental Policy Act **NEPA**

NFA No Further Action NGB National Guard Bureau

NPDES National Pollution Discharge Elimination System

NPL **National Priorities List** OBG Open Burning Ground ODOW Ohio Department of Wildlife OE Ordnance and Explosives

OEPA Ohio Environmental Protection Agency

OHARNG Ohio Army National Guard OSC **Operations Support Command**

PA **Preliminary Assessment**

PBC Performace Based Contracting **PCB** Poly Chlorinated Biphenals POL Petroleum. Oil & Lubricants

RA Remedial Action

Remedial Action - Construction RA(C) Remedial Action - Operation RA(O)

Acronyms & Abbreviations

RAB Restoration Advisory Board

RCRA Resource Conservation and Recovery Act

RD Remedial Design

RDX hexahydro-1,3,5-trinitro-1,3,5-triazine

REM Removal

RI Remedial Investigation
RIP Remedy in Place
ROD Record of Decision

RRSE Relative Risk Site Evaluation

RTLS Ravenna Training and Logistics Site RVAAP Ravenna Army Ammunition Plant

SAIC Science Application International Corporation

SI Site Inspection

SVOC Semi-Volatile Organic Compounds **SWMU** Solid Waste Management Unit

TAPP Technical Assistance for Public Participation

TNT 2,4,6-trinitrotoluene

TPH Total Petroleum Hydrocarbons

USACE United States Army Corps of Engineers

USACHPPM United States Army Center for Health Promotion and Preventive Medicine

USAEC United States Army Environmental Center

USAEHA United States Army Environmental Hygiene Agency (changed to USACHPPM)
USATHMA United States Army Toxic and Hazardous Materials Agency (replaced by AEC)

UST Underground Storage Tank
UXO Unexploded Ordnance
VOC Volatile Organic Compounds
WBG Winklepeck Burning Ground



Ravenna Army Ammunition Plant Installation Action Plan FY04

MARK C. PATTERSON Facility Manager Ravenna AAP

KENNETH E. WIGGANS
Chief, Oversight North Branch
US Army Environmental Center

RANDALL J. CERAR
Chief, Cleanup Division
US Army Environmental Center



STATUS

RVAAP is not a NPL site. RVAAP had submitted a Part B permit application to U. S. and Ohio Environmental Protection Agencies. The application covered the installation's interim status RCRA sites. The permit application was withdrawn during the 3rd quarter of FY94. The installation is currently negotiating Director's Findings and Orders with the Ohio EPA to cover future hazardous waste activities needed for closure of RVAAP.

NUMBER OF SITES:

51 AEDB-R sites

29 Active ER, A Eligible Sites

4 Sites under PBC

18 Response Complete under ER,A

0 MMRP Sites

DIFFERENT SITE TYPES:

3 Burn Areas
1 Contaminated Building
1 Contaminated Building
3 Disposal Pit/Dry Wells
1 Firing Range
2 Industrial Discharges

3 Landfills 1 Pistol Range 1 Pesticide Shop 4 Storage Areas

6 Spill Site Area 9 Surface Impoundment/Lagoons 6 Waste Treatment Plants 2 Underground Storage Tanks 3 Other (RVAAP-17, 35, 38) 3 Above Ground Storage Tanks

1 Explosive Ordnance Disposal Area 1 Unexploded Munitions/Ordnance

CONTAMINANTS OF CON-

CERN:

Explosives, Heavy Metals, Propellants, Pesticides (PCBs), SVOCs, VOCs

MEDIA OF CONCERN:

Groundwater, Soil, Surface Water, Sediment

COMPLETED REM/IRA/RA:

RVAAP-47, Building T-5301 IRA RVAAP-03, Open Demo Area #1

CURRENT IRP PHASES

(per funding):

RI/FS at 16 sites PBC at 4 sites

RD at 2 sites

LTM at 1 sites

PROJECTED IRP PHASES

(per funding):

RI/FS at 21 sites

RA(O) at 1 site

RD at 18 sites LTM at 23 sites RA at 19 sites PBC at 4 sites

IDENTIFIED POSSIBLE REM/IRA/

RA:

RVAAP-04, 05, 06, 08, 09 (PBC), 10 (PBC), 11 (PBC), 12, 13, 16, 19,

33, 36, 38, 39, 40, 41, 42, 43, 45, 46, 49, 50

FUNDING:

PRIOR YEAR FUNDS \$31,797,422.32 <u>FUTURE REQUIREMENTS</u> \$36,718,000

TOTAL

\$ 68,515,422.32

DURATION:

YEAR OF IRP INCEPTION: 1989
PROJECTED COMPLETION DATE OF ALL RAS: 2014
YEAR OF IRP COMPLETION 2015+

Installation Information

SITE DESCRIPTION:

The Ravenna Army Ammunition Plant (RVAAP) is located on 21,419 acres in Portage and Trumbull Counties, Ohio. Warren, Ohio is located 7 miles to the east of RVAAP and Kent, Ohio is located 15 miles to the west. The Operations Support Command (OSC) transferred control and operation of 16,164 acres to the National Guard Bureau in May 1999. In March 2002, an agreement was signed to immediately transfer an additional 3,774 uncontaminated acres to the National Guard with the remaining acreage to be transferred as restoration of the AOCs is completed.

COMMAND ORGANIZATION:

INSTALLATION: Ravenna Army Ammunition Plant, Commander's Representative and National Guard Bureau

INSTALLATION MODIFIED CARETAKER CONTRACTOR: Toltest Inc.

IRP EXECUTING AGENCIES:

INVESTIGATION PHASE: U.S Army Corps of Engineers, Louisville District **ACTION PHASE:** U.S Army Corps of Engineers, Louisville District

REGULATORY PARTICIPATION:

FEDERAL: U.S. Environmental Protection Agency, Region V **STATE:** Ohio Environmental Protection Agency (Ohio EPA)

REGULATORY STATUS:

- RCRA Interim Part A Permit
- Signing of the Orders will also transfer regulation of the RCRA groundwater unit at Ramsdell Quarry and Open Demolition Area #2 and all media at the Deactivation Furnace to the CERCLA program. The source of most contamination at or adjacent to the sites originates from unregulated activities that took place from 1940 to 1980. Cleanup of the sites will be more efficient once the sites are placed under a single regulatory program.

Installation Description

HISTORY

RVAAP is a government-owned, contractor-operated (GOCO) U.S. Army BRAC facility. In FY 1993, the mission of RVAAP was changed from inactive-maintained to modified caretaker status (limited mission). Toltest, Inc. is the current modified caretaker contractor. The current mission is storage of bulk explosives and propellants. The installation is contained within an 11 mile long, 3.5 mile wide tract and is bounded by State Route 5, the Michael J. Kirwan Reservoir, and the CSX System Railroad on the south; State Route 534 on the east; the Garrettsville and Berry roads on the west; and the Conrail Railroad on the north.

In August 1940, a tract of land covering 25,000 acres was purchased by the United States Government in the northeastern part of Ohio in Portage and Trumbull counties. Construction of the plant started in September 1940 with the Hunkin-Conkey Construction Company as the principal contractor, Wilbur Watson and Associates as the principal engineers, and the Atlas Powder Company as the operating contractor and consultant. The facility was completed and commenced operations during December 1941/January 1942, with the primary missions of depot storage and ammunition loading. To accomplish these two missions, the installation was divided into two separate units, the Portage Ordnance Depot and the Ravenna Ordnance Plant. The Portage Ordnance Depot's primary mission was depot storage of munitions and components, while the Ravenna Ordnance Plant's mission was ammunition loading. In August 1943, the installation was redesignated the Ravenna Ordnance Center, and again in November 1945 as the Ravenna Arsenal.

Facilities were operated by the Atlas Powder Company from September 1940 until the end of World War II. The operation of the plant was turned over to the Ordnance Department. From 1946 to 1949, the ammonium nitrate line was operated by the Silas Mason Company for the production of ammonium nitrate fertilizer.

The plant was placed in standby status in 1950 and operations were limited to renovation, demilitarization, and normal maintenance of equipment, along with storage of ammunition and components.

Beginning in April 1951, facility operations were contracted with Ravenna Arsenal, Inc., a subsidiary of the Firestone Tire and Rubber Company of Akron, Ohio.

The plant was reactivated during the Korean Conflict for the loading and packing of major caliber shells and components. In July 1954, the Plum Brook Ordnance Works of Sandusky, Ohio and the Keystone Ordnance Works of Meadville, Pennsylvania were made satellites to Ravenna. All production ended in August 1957, and in October 1957, the installation was again placed in a standby condition. The Plum Brook Plant ceased to be under the jurisdiction of Ravenna in March 1958. The Keystone Ordnance Works was transferred to the General Services Administration in July 1959.

Rehabilitation work started in October 1960 to establish facilities in the ammonium nitrate line for the processing and explosive melt-out of bombs. These operations commenced in January 1961, thereby establishing the first operation of this type in the ammunition industry. In July 1961, the plant was again deactivated and in November 1961, the installation was divided once again. The industrial portion was redesignated as the Ravenna Ordnance Plant and the entire facility was designated the Ravenna Army Ammunition Plant. The RVAAP was once again reactivated in May 1968 to load, assemble, and pack (LAP) munitions on three load lines and two component lines in support of the Southeast Asian Conflict. These facilities were subsequently deactivated in August 1972. A mission for the demilitarization of the M71A1 90MM projectile extended from June 1973 until March 1974.

In October 1982, the Physics International Company, a subsidiary of Rockcor, Inc., purchased Ravenna Arsenal, Inc. from the Firestone Company. In June 1985, Rockcor Inc. was purchased by the Olin Corporation.

Demilitarization of various munitions continued on a periodic basis through 1992. In FY 1993, the installation's status changed from inactive-maintained to modified caretaker. On October 1, 1998, R&R International, Inc. took over as the installation's contractor (R&R was later replaced by Toltest, Inc).

The Operations Support Command (OSC) transferred control and operation of 16,164 acres to the National Guard Bureau in May 1999. In March 2002, an agreement was signed to immediately transfer an additional



3,774 uncontaminated acres to the National Guard with the remaining acreage to be transferred as restoration of the AOCs is completed.

REGULATORY STATUS

RVAAP is not on the U.S. EPA NPL, although it is in the U.S. EPA's CERCLIS database. Management of the IRP sites follows CERCLA requirements. There are a number of other regulatory programs addressing other non-IRP sites.

RVAAP received a RCRA Part A permit in 1980 for the storage and treatment of off-spec munitions and munitions-related waste. RVAAP submitted a RCRA Part B permit application in 1992 for the installation's Open Burning and Open Detonation Grounds and a hazardous waste storage building. The permit application was withdrawn during the 3rd quarter of FY 1994. The closure of the storage units and the open burn trays in Winklepeck Burning Grounds was completed and approved in 1998. Three 90-day hazardous waste storage areas were also officially closed.

A closure plan was developed for the Demolition Area #2 (RVAAP-04) in 1998, but has been reconsidered at this time. The site has been used since 1941 for treatment of explosive waste and ordnance by burning and detonation. The need for a treatment unit, to support the IRP and other projects, to detonate unexploded ordnance (UXO) was not known at the time the plan was developed. Subsequently, UXO has been found at several areas at RVAAP. Some of the areas are associated with IRP sites, while others are strictly a UXO concern. More UXO will almost certainly be found during future environmental investigations, remediation activities, and National Guard exercises. These circumstances have demonstrated the need for the use of a previously permitted RCRA unit where UXO can be detonated. The Army and Ohio EPA are currently developing Director's Findings and Orders to authorize continued use of Demolition Area #2 for purposes of supporting environmental restoration.

Contamination Assessment

The contamination at RVAAP originated from past industrial activities associated with the production and demilitarization of large caliber shells, gravity bombs, and parts for these munitions. RVAAP produced munitions during World War II and the Korean and Vietnam Wars. The industrial operations at RVAAP consisted of 12 production areas known as Load Lines. Load Lines 1 through 4 (melt-pour Lines) were the primary sources of secondary explosives contamination such as TNT, HMX and RDX, which were melted and poured into shell and bomb cavities. Load Line 1 and 12 were used for demilitarization of shells. Load Line 1 was used to produce and recondition tank mines. Workers would periodically use steam and hot water to hose down equipment and the floors and walls of buildings contaminated with explosive dust, spills, and vapors. The explosive-contaminated water from the cleaning, known as "pink water", then drained out doorways and through floor drains onto the soils surrounding the buildings or was discharged into open ditches or ponds after being filtered through saw dust to remove suspended explosives. Waste explosives from the melt pour Lines were routinely disposed of by open burning and detonation at other sites on the installation.

Load Lines 5 through 11 (fuze and booster) were used to manufacture fuzes, primers, and boosters while Load Line 12 housed the ammonium nitrate plant. Potential contaminants in Lines 5 through 11 include lead azide, mercury fulminate, lead styphnate, black powder, heavy metals, TNT, and Composition B. The amount of explosives used at the fuze and booster Lines was much less than that used at the melt-pour Lines because of the types of small munitions components being made there. Also, the operations did not create as much waste and were cleaner due to the special handling procedures needed when working with the highly shock and heat sensitive primary explosives. Load Line 12 produced ammonium nitrate for explosives, fertilizers and aluminum chloride. It also was periodically used for demilitarization projects involving the melt-out of TNT and other secondary explosives from the cavities of bombs and shells. As in the other melt pour Lines, these activities resulted in pink water being released to the soils, ditches, and ponds in and around the Line. Other types of contaminated sites associated with past industrial activities at RVAAP include landfills, testing facilities, dumps, burial sites, a pistol range, storage facilities, a scrap yard, and decontamination buildings. Although not present at every one of these sites, the contaminants of potential concerns include primary and secondary explosives, propellants, heavy metals, volatile and semivoltile organics, PCBs, and pesticides. Industrial activities ceased in 1992 when RVAAP was declared excess.

RVAAP started the IRP in 1989. Currently there are 32 active sites and 4 PBC sites in the program. The sites were given a RRSE rating of high, medium, or low based on the results of limited sampling in 1996 and 1998. Sampling has been done of the soil, sediment, surface, and groundwater at many of the high sites and a some of the medium sites as part of the remedial investigation process during the past 7 years.

Preliminary well sampling, conducted by Ohio EPA in 1997 and 1998, showed no off-post explosives contamination of residential wells.

A Phase I RI examined 11 high priority sites identified as RVAAP-04, 05, 08, 09, 10, 11, 12, 13, 18, 19, and 29. A final RI report was issued in 1997. The study concluded that Load Lines 1-4, and 12 appeared to be the most contaminated, contaminants were probably not migrating far from the sources in significant concentrations, and the RRSE score of three sites (RVAAP-13, 19, 29) should be lowered to medium. The report recommended further study in the form of a Phase II RI at these sites to determine the nature, extent and significance of contamination.

Investigation of Winklepeck Burning Grounds (WBG) is the furthest along of all the AOCs. The 200-acre site has high explosives and heavy metals soil contamination at many of the 70 burn pads. The concentrations are highest on the pads in the northeast and northwest. Soils at seven of the pads were identified as having significant risk for humans for at least one of the seven evaluated receptors. Significant soil contamination has been found to a depth of 6 feet at some of the most heavily used pads. Soils contamination between the pads was occasionally found. The study identified at least one animal species at every pad that would be potentially at risk. A field truthing ecological study of WBG was started in order to further evaluate the results of the screening risk assessment. It is nearing completion. Low levels of explosives were detected in the groundwater at two wells and the sediment at WBG. No COPCs were identified for human or ecological receptors exposed to

Contamination Assessment

surface water.

Phase II field sampling has been completed at the four melt-pour Lines. A final report for Load Line 1 and draft reports for Load Lines 2, 3 and 4, and the draft final report for LL-12 have been issued. Results have for the most part confirmed initial beliefs that explosives and heavy metals are the most common contaminants and are generally located immediately around buildings and in the ditches and ponds draining the sites. Less common contaminants include PCBs and propellants. These same contaminants have been detected in the water and sediment within the storm sewers in the past. On-post wells located to the southeast of Load Line 2 near the perimeter have shown trace amounts of explosives. Of the fuze and booster Lines, only Load Line 11 has undergone extensive sampling to determine the nature and extent of contamination. Although a report has not been issued, the data indicates that lead, arsenic, antimony, chromium, PCBs, and some other organics appear to be the most common contaminants. Very low levels of explosives were sporadically detected. High lead levels have been detected in the sediment from the sanitary sewers. Surface and sediment samples indicate significant levels of contaminants are not migrating from the site. This is consistent with the results from limited SI sampling of Load Lines 6, 9, and 10 in the spring of 2002 and the RRSE data collected in 1996 and 1998 for the other fuze and booster Lines. The preliminary-draft RI reports for Load Lines 2, 3 and 4 are under review.

Varying amounts of RI data are also available for some of the other AOCs used to support the main production activities. Limited data available from earlier efforts again show explosives and heavy metals to be the principle contaminants at sites used to burn, dump, or bury explosive waste from the Load Lines. These contaminants are most frequently found in the soils at Demolition Area #2 and Erie Burning Grounds, areas used to detonate and burn waste explosives. Erie has in recent years existed as a shallow impoundment and wetlands, resulting in explosives, metals and some organics being detected in the surface water and sediment at and downstream of the site. Explosives have been detected in the RCRA groundwater well samples taken at OD 2 where large amounts of UXO and OE scrap are still present.

Data currently being evaluated for the Cobb Ponds, which were settling basins for Load Line 3 and 12 effluent, indicate low levels of explosives, organics, and metals. Generally, contaminants are not present in the ground and surface water. After completion of a UXO removal operation at OD 1, confirmation samples of the soils had no detections of explosives and some metals were only slightly above background. The explosive RDX (below reporting limit) was detected at very low levels in the surface water downstream of the site near the installation boundary. Central Burn Pits, an area used to burn electrical components, dunnage, and other non explosive waste, has shown significant detections of lead, arsenic, antimony, cyanide, silver, and pesticides in the soil. Lead, cyanide, arsenic, and pesticides were noted in the sediment while surface and groundwater had slightly elevated arsenic. The data is currently being evaluated and a report is expected to be completed in spring 2004.

In 2003, a Perforance Based Contract (PBC) was awarded to Shaw Environmental to complete the soil remediation at Load Lines 1, 2, 3 and 4. Remedial investigation at Load Lines 2, 3 and 4 will be completed; remedial technologies will be screened and an approved method will be selected and implemented to eliminate any threat to human health or the environment from contaminated soils and sediments. Ravenna AAP was one of the first Army installations to implement PBC, the Army's newesy stategy to accelerate clean up programs nationwide. The project will result in an interim remedy. Additional investigations of the soils under the inaccessable portions of the buildings will be needed. Results of the investigations will be used to determine if additional remedial action is needed to make the sites safe for training by the OARNG.

| | Previous S | tudies |
|--|-------------|----------|
| Title | Author | Date |
| Installation Assessment of Ravenna Army Ammunition Plant. Report No. 132 | USATHMA | Nov-78 |
| Ravenna Army Ammunition Plant RCRA Facility Assessment Draft RR/VSI Report | Jacobs | Oct-89 |
| The same of the sa | Engineering | |
| | Group, Inc. | |
| Hazardous Waste Management Study No. 37-26-0442-84: Phase 2 of AMC Open | USAEHA | Oct-89 |
| Burning/Open Detonation Groundwater Evaluation | OSC/Specpro | |
| Facility-Wide Safety and Health Plan for the Ravenna Army Ammunition Plant | OSC/mkm | Feb-96 |
| Preliminary Assessment for the Characterization of Areas of Contamination | OSC/mkm | Feb-96 |
| Action Plan for the Ravenna Army Ammunition Plant | OSC/mkm | Mar-96 |
| Facility-Wide Sampling and Analysis Plan for the Ravenna Army Ammunition Plant | OSC/Specpro | Apr-96 |
| Phase 1 Remedial Investigation Sampling and Analysis Plan Addendum for High Priority | OSC/Specpro | Jul-96 |
| Areas of Concern for the Ravenna Army Ammunition Plant | | |
| Phase 1 Remedial Investigation Site Safety and Health Plan Addendum for High Priority Areas of Concern for the Ravenna Army Ammunition Plant | OSC/mkm | Jul-96 |
| Investigation-Derived Waste Characterization and Disposal Plan for the Phase I RI of High | USACE | Dec-96 |
| Priority Areas of Concern at RVAAP | OSC/mkm | |
| Public Meeting Briefing - Phase I RI of High Priority AOCs at the RVAAP | USACE | Sep-97 |
| Quality Control Plan for the phase II RI for Winklepeck Burning Grounds at RVAAP | USACE | Jan-98 |
| Sampling and Analysis Plan Addendum for the Phase II Remedial Investigation for Winklepeck | | Jan-98 |
| Burning Grounds at the Ravenna Army Ammunition Plant | | |
| Remedial Investigation Report for the Phase I Remedial Investigation of High Priority Areas of | | Feb-98 |
| Concern at the Ravenna Army Ammunition Plant. Volume I Main Text | | |
| Remedial Investigation Report for the Phase I Remedial Investigation of High Priority Areas of | | Feb-98 |
| Concern at the Ravenna Army Ammunition Plant. Volume II Appendixes A-K | | |
| Geophysical Survey Results of Mustard Agent Burial Site at RVAAP, Edition 2 | USACE | Mar-98 |
| Safety and Health Plan Addendum for the Phase II Remedial Investigation of the Winklepeck | 00,102 | Apr-98 |
| Burning Grounds and Determination of Facility-Wide Background | | 7 |
| Geophysical Survey Results of mustard Agent Burial Site 1 at RVAAP, Edition 1 | USACE | Apr-98 |
| SAP Addendum for the Phase II RI of the Winklepeck Burning Grounds and Determination of | USACE | Apr-98 |
| facility-Wide Background at the RVAAP | 00/102 | , .p. 00 |
| RCRA Closure Field Investigation Report for the Deactivation Furnace Area, Open Detonation | USACE | Jun-98 |
| Area, Building 1601, and Pesticides Building at RVAAP | 00/102 | July 00 |
| SAP and SSHP Addendum for the Groundwater Investigation of the Former Ramsdell Quarry | USACE | Jun-98 |
| Landfill | OUNCE | our so |
| Hazardous Medical Waste Study RRSE for Newly Added Sites at RVAAP | USACE | Oct-98 |
| October 1998 Quarterly Monitoring Report, Ramsdell Quarry Groundwater Investigation | USACE | Oct-98 |
| Initial Phase Report Groundwater Investigation Ramsdell Quarry at RVAAP | USACE | Jan-99 |
| Initial Phase Report, Groundwater Investigation, Ramsdell Quarry Landfill | USACE | Jan-99 |
| February 1999 Quarterly Monitoring Report, Ramsdell Quarry Groundwater Investigation | USACE | Feb-99 |
| Quarterly Monitoring Report, Ramsdell Quarry Groundwater Investigation | USACE | Apr-99 |
| Phase II RI Report for the Winklepeck Burning Grounds at RVAAP | USACE | Aug-99 |
| Sampling and Analysis Plan Addendum No. 1 for the Phase II RI of Load Line | USACE | Aug-99 |
| SAP Addendum No. 1 for the Phase II RI Load Line 1 | USACE | Aug-99 |
| Environmental Information Management Needs Assessment | USACE | Sep-99 |
| SAP Addendum No. 1 for Phase 1 RI of Demo Area 1 at RVAAP | USACE | Oct-99 |
| SSHP Addendum No. 1 for Phase I RI of Demo Area 1 at RVAAP | USACE | Oct-99 |
| Draft- Vegetation Methods for Ground-Truthing of Ecological Risk at Winklepeck Burning | USACE | Dec-99 |
| Grounds at the RVAAP, Draft | JUAUL | DGC-33 |
| Small Mammal Methods for Ground-Truthing of Ecological Risk at Winklepeck Burning | USACE | Dec-99 |
| Grounds at the RVAAP | UUAUE | Dec-99 |
| Sampling and Analysis Plan for the Interim Removal Action, Decontamination and Demolition | OSC | Feb-00 |
| of Building T-5301(AOC 47) | | |

| Site Specific Safety and Health Plan for the Interim Removal Action, Decontamination and OSC Feb-00 Demolition of Building T-5301 (AOC 47) Work Plan & Sampling and Analysis for the Bioremediation Pilot Study for Soils from Former Bidg. FJ 904 at Load Line 12 (AOC 12) Tontaf-Final Completion Report for the Bioremediation Pilot Study for Soils from Former Bidg. FJ 904 at Load Line 12 (AOC 12) Tontaf-Final Completion Report for the Bioremediation Pilot Study for Soils from Former Bidg. FJ 904 at Load Line 12 (AOC 12) SAP and SSHP Addendum No. 2 for the Biological Measurements at Winklepeck Burning USACE May-00 Grounds at RVAAP Facility-Wide SAP and Facility-Wide SSHP for Environmental Investigations for RVAAP USACE Jul-00 Report Groundwater Investigation at Ramsdell Quarry at RVAAP Report Groundwater Investigation at Ramsdell Quarry at RVAAP Report Groundwater Investigation at Load Line 1 USACE Sep-00. SAP for Phase II R Load Line 12 at RVAAP SSHP for Phase II R Load Line 12 at RVAAP SSHP for Phase II RI Load Line 12 at RVAAP OE/UXO Locating, Removal and Disposal at the Open Detonation Area #2 OSC Sep-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Jan-01 Site Safety and Health Plan for the Phase II R | Title | Author | Date |
|---|--|----------|--------|
| Demolition of Building T-5301 (AOC 47) Work Plan & Sampling and Analysis for the Bioremediation Pilot Study for Soils from Former Didg, FJ 904 at Load Line 12 (AOC 12) Draft-Final Completion Report for the Bioremediation Pilot Study for Soils from Former Bildg. FJ 904 at Load Line 12 (AOC 12) SAP and SSHP Addendum No. 2 for the Biological Measurements at Winklepeck Burning Grounds at RVAAP Facility-Wide SAP and Facility-Wide SSHP for Environmental Investigations for RVAAP Facility-Wide SAP and Facility-Wide SSHP for Environmental Investigations for RVAAP Facility-Wide SAP and Facility-Wide SSHP for Environmental Investigations for RVAAP Facility-Wide SAP and Facility-Wide SSHP for Environmental Investigations for RVAAP Facility-Wide SAP and Facility-Wide SSHP for Environmental Investigations for RVAAP Sampling and Analysis Plan Addendum No. 2 for the Phase II RI of Load Line 1 SACE SEP-00 SSMP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE SSHP for Phase II RI Load Line 12 at RVAAP USACE Occ. 00-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct. 00 Ste Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct. 00 SSRP for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct. 00 SSC SAP-01 Sampling and Anal | | | |
| Work Plan & Sampling and Analysis for the Bioremediation Pilot Study for Soils from Former Bldg. F. 1904 at Load Line 12 (AOC 12) Draft-Final Completion Report for the Bioremediation Pilot Study for Soils from Former Bldg. F. 1904 at Load Line 12 (AOC 12) Draft-Final Completion Report for the Bioremediation Pilot Study for Soils from Former Bldg. F. 1904 at Load Line 12 (AOC 12) Mar-00 FL 904 at Load Line 12 (AOC 12) May-00 Grounds at RVAAP Facility-Wide SSHP for Environmental Investigations for RVAAP USACE Report Groundwater Investigation at Ramsdell Quarry at RVAAP Report Groundwater Investigation at Ramsdell Quarry at RVAAP Report Groundwater Investigation at Ramsdell Quarry at RVAAP Report Brain In Load Line 12 at RVAAP Report Phase II RI Load Line 12 at RVAAP SAP for Phase II RI Load Line 12 at RVAAP SAP for Phase II RI Load Line 12 at RVAAP OE/UXO Locating, Removal and Disposal at the Open Detonation Area #2 OSC Sep-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) SSC Oct-00 Work Plan for the Remedial Investigation at Central Burn Pits SSC Aug-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits SSC Aug-01 Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) SSC Oct-00 SSC Jan-01 Sampling and Analysis for the | | | |
| Bidg. FJ 904 at Load Line 12 (ACC 12) | | OSC | Mar-00 |
| Draft-Final Completion Report for the Bioremediation Pilot Study for Soils from Former Bldg. Draft Ship 4 at Load Line 12 (ACC 12) | | | |
| SAP and SSHP Addendum No. 2 for the Biological Measurements at Winklepeck Burning Grounds at RVAAP Facility-Wide SAP and Facility-Wide SSHP for Environmental Investigations for RVAAP USACE Report Groundwater Investigation at Ramsdell Quarry at RVAAP USACE Sep-00 SAP for Phase II RI Load Line 12 at RVAAP USACE Sep-00 SAP for Phase II RI Load Line 12 at RVAAP USACE Sep-00 SAP for Phase II RI Load Line 12 at RVAAP USACE Sep-00 SAP for Phase II RI Load Line 12 at RVAAP USACE Sep-00 OEAUXO Locating, Removal and Disposal at the Open Detonation Area #2 OSC Sep-00 OEAUXO Locating, Removal and Disposal at the Open Detonation Area #2 OSC OC-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Central Burn Pits OSC Apr-01 Sampling and Analysis Flan for the Remedial Investigation at Central Burn Pits OSC Apr-01 Work Plan for the Interim Removal Action of the Paris-Windham Road Dump (AOC Sampling and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Apr-01 Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Oct-00 Sa | | OSC | Mar-00 |
| Grounds at RVAAP Report Groundwater Investigation at Ramsdell Quarry at RVAAP Report Groundwater Investigation at Load Line 11 (ADC 44) Report Groundwater Investigation at Load Line 11 (ADC 44) Report Groundwater Report Investigation at Load Line 11 (ADC 44) Report Groundwater Report Investigation at Load Line 11 (ADC 44) Report Groundwater Report Investigation at Load Line 11 (ADC 44) Report Groundwater Report Investigation at Load Line 11 (ADC 44) Report Groundwater Report Investigation at Load Line 11 (ADC 44) Report Groundwater Report Investigation at Load Line 11 (ADC 44) Report Groundwater Report Investigation at Load Line 11 (ADC 44) Report Groundwater Report Investigation at Load Line 11 (ADC 44) Report Groundwater Report Investigation at Load Line 11 (ADC 44) Report Groundwater Report Re | FJ 904 at Load Line 12 (AOC 12) | | |
| Grounds at RVAAP Facility-Wide SAP and Facility-Wide SSHP for Environmental Investigations for RVAAP USACE Aug-00 Report Groundwater Investigation at Ramsdell Quarry at RVAAP USACE Sampling and Analysis Plan Addendum No. 2 for the Phase II Rt of Load Line 1 USACE Sep-00 SSHP for Phase II RL Load Line 12 at RVAAP USACE SSHP for Phase II RL Load Line 12 at RVAAP USACE SSHP for Phase II RL Load Line 12 at RVAAP USACE SSHP for Phase II RL Load Line 12 at RVAAP USACE SSHP for Phase II RL Load Line 12 at RVAAP USACE SSHP for Phase II RL Load Line 12 at RVAAP USACE SSHP for Phase II RL Load Line 12 at RVAAP USACE SSHP for Phase II RL Load Line 12 at RVAAP USACE SSHP OO Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) USC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) USC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) USC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) USC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) USC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) USC Oct-00 Sampling and Analysis rothe Phase II Remedial Investigation at Central Burn Pits USC | | USACE | May-00 |
| Report Groundwater Investigation at Ramsdell Quarry at RVAAP Sampling and Analysis Plan Addendum No. 2 for the Phase II RI of Load Line 1 USACE Sep-00 SSHP for Phase II RI Load Line 12 at RVAAP USACE Sep-00 SSHP for Phase II RI Load Line 12 at RVAAP USACE Sep-00 SSHP for Phase II RI Load Line 12 at RVAAP USACE Sep-00 SSHP for Phase II RI Load Line 12 at RVAAP USACE Sep-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sompling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sompling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sompling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Central Burn Plts OSC Apr-01 Sompling and Analysis Plan for the Remedial Investigation at Central Burn Plts OSC Apr-01 Sompling and Analysis for the Phase II Remedial Investigation at Central Burn Plts OSC Aug-01 Sompling and Analysis for the Phase II Remedial Investigation at Central Burn Plts OSC Aug-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Plts OSC Aug-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Plts OSC Aug-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jul-01 Sampling and Analysis for the Interim Removal Action at | Grounds at RVAAP | | |
| Sampling and Analysis Plan Addendum No. 2 for the Phase II RI of Load Line 1 USACE Sep-00 SAP for Phase II RI Load Line 12 at RVAAP USACE Sep-00 DE/UXO Locating, Removal and Disposal at the Open Detonation Area #2 OSC Sep-00 DE/UXO Locating, Removal and Disposal at the Open Detonation Area #2 OSC Sep-00 DE/UXO Locating, Removal and Disposal at the Open Detonation Area #2 OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Oct-00 Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Agr-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action Decontamination and Demolition of Building T- S301(AOC 47) OSC | Facility-Wide SAP and Facility-Wide SSHP for Environmental Investigations for RVAAP | USACE | Jul-00 |
| SAP for Phase II RI Load Line 12 at RVAAP SSHP for Phase II RI Load Line 12 at RVAAP OFAUXO Locating, Removal and Disposal at the Open Detonation Area #2 OSC Sep-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Central Burn Pits OSC Aug-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Sampling and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jan-01 Sampling and Analysis Addendum for the Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial | Report Groundwater Investigation at Ramsdell Quarry at RVAAP | USACE | Aug-00 |
| SSHP for Phase II RI Load Line 12 at RVAAP OE/UXO Locating, Removal and Disposal at the Open Detonation Area #2 OSC Sep-00 OE/UXO Locating, Removal and Disposal at the Open Detonation Area #2 OSC Sep-00 Osc Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC OSC Apr-01 Sampling and Analysis Plan for the Phase II Remedial Investigation at Load Line 11 (AOC 44) OSC Apr-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T- S301(AOC 47) Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Site Safety and Health Plan for the Remedial/Design Remova | Sampling and Analysis Plan Addendum No. 2 for the Phase II RI of Load Line 1 | USACE | Sep-00 |
| OECLIVO Locating, Removal and Disposal at the Open Detonation Area #2 | SAP for Phase II RI Load Line 12 at RVAAP | | Sep-00 |
| Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Phase II Remedial Investigation at Central Burn Plts OSC Apr-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Plts OSC Aug-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Plts OSC Aug-01 Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T-OSC Feb-00 Sour (AOC 47) Source Aug-01 Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis Addendum for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Remova | | | Sep-00 |
| Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC OSC Apr-01 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Apr-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis Addendum for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Remedial/Design Removal Action of the Paris-Upper Sampling and Analysis Addendum for the R | OE/UXO Locating, Removal and Disposal at the Open Detonation Area #2 | | Sep-00 |
| Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC OSC Apr-01 \$51) Work Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T- S301(AOC 47) Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Feb-00 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Work Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Apr-02 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Apr-02 Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Des | | OSC | Oct-00 |
| Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Work Plan for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC SC Apr-01 51) Work Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T-Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Draft Groundwater Quality Assessment Program for the Remedial/Design Removal Action of the Paris-OSC Apr-02 Windham Road Dump (AOC 51) Site Safety and Health Plan for the Remedial/Design Removal Action of the Paris-OSC Apr-02 Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris-OSC Apr-02 Windham Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action a | | | Oct-00 |
| Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Oct-00 Oct-00 Ost-00 Osc Oct-00 Osc Opt-00 Osc Oct-00 Osc Opt-01 Osc Osc Opt | Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) | | Oct-00 |
| Sampling and Analysis Plan for the Remedial Investigation at Load Line 11 (AOC 44) OSC Apr-01 5/1) Work Plan for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC 5/1) Work Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T-Soc Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jul-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Apr-02 Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris-OSC Apr-02 Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 (AOC 34) Site Specific Safety an | | | |
| Work Plan for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC SC 51) Mork Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T-OSC Sc Aug-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) Work Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Closure Report for the Interim Removal Action, Decontamination and Demolition of Building T-Sond (AOC 47) Draft Compliance Monitoring Program for the Open Detonation Area #2 Draft Compliance Monitoring Program for the Open Detonation Area #2 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Nov-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Windham Road Dump (AOC 54) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for the Remedial/Doc 34) | Site Safety and Health Plan for the Remedial Investigation at Load Line 11 (AOC 44) | | Oct-00 |
| Work Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T-OSC Feb-00 S301(AOC 47) Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris-OSC Apr-02 Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris-OSC Apr-02 Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 (AOC 34) Interim Removal Action for Load Line #11 OE/UXO Removal and Interim Removal Action Report for the Open Demolition | | | Oct-00 |
| Work Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T- Side Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T- Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Pond Closure Report for the Interim Removal Action, Decontamination and Demolition of Building T- Side (AOC 47) Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jul-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Nov-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 OE/UXO Removal and Interim Removal Action Report for the Open Demo | Work Plan for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC | OSC | Apr-01 |
| Sampling and Analysis for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T- 5301(AOC 47) Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) Soc Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) Work Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Open Detonation and Demolition of Building T- Soc Jul-01 Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jun-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Nov-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand | | | |
| Site Safety and Health Plan for the Phase II Remedial Investigation at Central Burn Pits OSC Aug-01 Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T- 5301(AOC 47) Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Work Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Pond Closure Report for the Interim Removal Action, Decontamination and Demolition of Building T- Site Safety and Health Plan for the Open Detonation Area #2 OSC Jul-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Nov-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck SAIC May-02 Burning Grounds | Work Plan for the Phase II Remedial Investigation at Central Burn Pits | | Aug-01 |
| Work Plan for the Interim Removal Action, Decontamination and Demolition of Building T- 5301(AOC 47) Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) Work Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Site Safety and Health Plan for the Open Detonation and Demolition of Building T- 5301 (AOC 47) Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jun-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Nov-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 Bampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck SAIC May-02 Burning Grounds | | | Aug-01 |
| Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Work Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Site Safety and Health Plan for the Open Detonation Area #2 OSC Jul-01 Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jun-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Nov-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck SAIC May-02 Burning Grounds | | | |
| Work Plan for the Interim Removal Action at Load Line 11 (AOC 44) Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) Work Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Closure Report for the Interim Removal Action, Decontamination and Demolition of Building T- 5301 (AOC 47) Draft Compliance Monitoring Program for the Open Detonation Area #2 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Jun-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 Creek Disposal Road Landfill (AOC 34) May-02 Burning Grounds | • | OSC | Feb-00 |
| Sampling and Analysis for the Interim Removal Action at Load Line 11 (AOC 44) Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Work Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Open Detonation and Demolition of Building T- OSC Jul-01 Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jun-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Nov-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Interim Removal Action for Load Line #11 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck SAIC May-02 Burning Grounds | | | |
| Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) OSC Jan-01 Work Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Poral Compliance Monitoring Program for the Open Detonation Area #2 OSC Jul-01 Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jun-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Nov-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris-Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill OSC Apr-02 Greek Disposal Road Landfill (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Apr-02 Bampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck May-02 Burning Grounds | | | |
| Work Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond OSC Jul-01 Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs OSC Jul-01 Closure Report for the Interim Removal Action, Decontamination and Demolition of Building T- 5301 (AOC 47) Draft Compliance Monitoring Program for the Open Detonation Area #2 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Nov-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Windham Road Dump (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 OSC Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck SAIC May-02 Burning Grounds | | | |
| Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Closure Report for the Interim Removal Action, Decontamination and Demolition of Building T- 5301 (AOC 47) Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jun-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Apr-02 Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Apr-02 Creek Disposal Road Landfill (AOC 34) Apr-02 Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Apr-02 Apr-02 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck BAIC May-02 Barning Grounds | Site Specific Safety and Health Plan for the Interim Removal Action at Load Line 11 (AOC 44) | OSC | Jan-01 |
| Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Site Safety and Health Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond Closure Report for the Interim Removal Action, Decontamination and Demolition of Building T- 5301 (AOC 47) Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jun-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Apr-02 Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Apr-02 Creek Disposal Road Landfill (AOC 34) Apr-02 Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Apr-02 Apr-02 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck BAIC May-02 Barning Grounds | Work Plan for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond | OSC | Jul-01 |
| Pond Closure Report for the Interim Removal Action, Decontamination and Demolition of Building T- 5301 (AOC 47) Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jun-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Nov-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | Sampling and Analysis for the Phase II Remedial Investigation at Upper & Lower Cobbs Pond | OSC | Jul-01 |
| Pond Closure Report for the Interim Removal Action, Decontamination and Demolition of Building T- 5301 (AOC 47) Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jun-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill OSC Nov-01 Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | Cita Cafaty and Haalth Dlan for the Dhaga II Damadial Investigation at Unner 9 Lawer Cabba | 000 | lul 04 |
| Closure Report for the Interim Removal Action, Decontamination and Demolition of Building T- 5301 (AOC 47) Draft Compliance Monitoring Program for the Open Detonation Area #2 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | | 030 | Jul-01 |
| 5301 (AOC 47) Draft Compliance Monitoring Program for the Open Detonation Area #2 OSC Jun-01 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill OSC (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 DE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | | OSC | Jul-01 |
| Draft Compliance Monitoring Program for the Open Detonation Area #2 Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand OSC Apr-02 Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill OSC Apr-02 (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Apr-02 Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 DE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Apr-02 Bampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | · · | | 0 |
| Draft Groundwater Quality Assessment Program Report for the Ramsdell Quarry Landfill Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill OSC Apr-02 (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | | OSC | Jun-01 |
| Sampling and Analysis Addendum for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | | OSC | Nov-01 |
| Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill OSC (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | | OSC | Apr-02 |
| Windham Road Dump (AOC 51) Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill OSC (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | Windham Road Dump (AOC 51) | | |
| Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill OSC (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | Site Specific Safety and Health Plan for the Remedial/Design Removal Action of the Paris- | OSC | Apr-02 |
| Creek Disposal Road Landfill (AOC 34) Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill OSC (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck SAIC May-02 Burning Grounds | Windham Road Dump (AOC 51) | | |
| Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill OSC (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | Sampling and Analysis Addendum for the Remedial/Design Removal Action at the Sand | OSC | Apr-02 |
| Work Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill OSC (AOC 34) Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand OSC Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 Apr-02 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds | Creek Disposal Road Landfill (AOC 34) | | |
| Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds OSC Apr-02 Apr-02 SAIC May-02 | | OSC | Apr-02 |
| Creek Disposal Road Landfill (AOC 34) Interim Removal Action for Load Line #11 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds Apr-02 | (AOC 34) | | |
| Interim Removal Action for Load Line #11 OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds Apr-02 May-02 | Site Specific Safety and Health Plan for the Remedial/Design Removal Action at the Sand | OSC | Apr-02 |
| OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 Apr-02 Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds SAIC | Creek Disposal Road Landfill (AOC 34) | <u> </u> | |
| Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds SAIC May-02 | Interim Removal Action for Load Line #11 | | Apr-02 |
| Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck Burning Grounds SAIC May-02 | OE/UXO Removal and Interim Removal Action Report for the Open Demolition Area #1 | | Apr-02 |
| | Sampling and Analysis Plan Addendum #3, Biological Measurements at the Winklepeck | SAIC | May-02 |
| Work Plan and Sampling and Analysis Plan Agenda for the Phase II Remedial Investigation of Jun-02 | Burning Grounds | <u> </u> | |
| | Work Plan and Sampling and Analysis Plan Agenda for the Phase II Remedial Investigation of | | Jun-02 |
| Demolition Area 2 | Demolition Area 2 | | |

| Title | Author | Date |
|--|--------|--------|
| Technical Memorandum, Human Health and Ecological Risk Assessment Approarch for the | SAIC | Aug-02 |
| Load Line 1 and Load Line 2 Phase II Remedial Investigations- Revised Final | | |
| RVAAPs Facility Wide Human Health Risk Work Plan- Draft | CELRL | Sep-02 |
| RVAAPs Facility Wide Ecological Risk Work Plan- Draft | CELRL | Oct-02 |
| Report on the Biological Field Truthing Effort and Winklepeck Burning Grounds- Draft Final | SAIC | Nov-02 |
| | | |
| RVAAPs Facility Wide Surface Water Assessment Work Plan- Draft | CELRL | Dec-02 |
| Conceptual Plan For a Facility-Wide Groundwater Monitoring Program Plan For the RVAAP | | Aug-03 |
| Final Sampling and Analysis Plan Addendum for the Remedial Investigation at Load Line #6 | | Sep-03 |
| Final Sampling and Analysis Plan Addendum for the Remedial Investigation at Load Line #9 | | Sep-03 |
| Final Safety and Health Plan for the Remedial Investigation of Load Lines #6, and #9 | | Sep-03 |
| Samling & Analysis Plan Addenda for the Phase I/Phase II Remedial Investigation of the Fuse & Booster Quarry Landfill/Ponds at the RVAAP | | Oct-03 |
| Safety and Health Plan for the Phase I/Phase II Remedial Investigation of the Fuse & Booster | | Oct-03 |
| Quarry Landfill/Ponds at the RVAAP | | |
| Final Work Plan for the Remedial Design/Removal Action at the Paris-Windham Road Dump | | Nov-03 |
| Final Work Plan for the Remedial Design/Removal Action at the Sand Creek Dump | | Nov-03 |
| Final Phase II Remedial Investigatin Report for the Winklepeck Burning Grounds at the | SAIC | Jun-03 |
| RVAAP (with revised executive summary) | | |
| Draft Final Phase II Remedial Investigation Report for Load Line 12 at the RVAAP | SAIC | Oct-03 |
| Final Phase II Remedial Investigation Report for Load Line 1at the RVAAP | SAIC | Jun-03 |
| Preliminary Draft Phase II Remedial Investigation Report for Load Line 2 at the RVAAP | SAIC | May-03 |
| Preliminary Draft Phase II Remedial Investigation Report for Load Line 3 at the RVAAP | SAIC | May-03 |
| Preliminary Draft Phase II Remedial Investigation Report for Load Line 4 at the RVAAP | SAIC | May-03 |
| Preliminary Draft Supplemental Baseline Human Health Risk Assessment for Load Line 1 | SAIC | May-03 |
| Alternative Receptors at the RVAAP | | |
| Final Facility Wide Ecological Risk Work Plan | CELRL | Apr-03 |
| Draft Facility Wide Human Health Risk Work Plan (Final Due Dec 03) | CELRL | Apr-03 |
| Final Sampling and Analysis Plan Addendum No. 1 for the Phase II Remedial Investigation of | SAIC | Oct-03 |
| the Erie Burning Grounds at the RVAAP | | |
| Final Site Safety and Health Plan Addendum No. I for the Phase II Remedial Investigation of | SAIC | Oct-03 |
| the Erie Burning Grounds at the RVAAP | | |
| Final Sampling and Analysis Plan Addendum No. 1 for the Phase I Remedial Investigation of | SAIC | Oct-03 |
| the Ramsdell Quarry Landfill at the RVAAP | | |
| Final Site Safety and Health Plan Addendum No. I for the Phase I Remedial Investigation of | SAIC | Oct-03 |
| the Ramsdell Quarry Landfill at the RVAAP | | |
| Final RVAAP Facility Wide Surface Water Assessment Work Plan | CELRL | Jan-03 |
| Ravenna Army Ammunition Plant Community Relations Plan | CELRL | Sep-03 |

ER,A ELIGIBLE ACTIVE DSERTS SITES

RVAAP-01 RAMSDELL QUARRY LANDFILL

SITE DESCRIPTION

The Ramsdell Quarry Landfill is an unlined, 10-acre landfill in the bottom of an abandoned quarry. Water is ponded in the northern end of the quarry. During the period 1946 to 1950, the site was used as a surface-burning site to thermally treat waste explosives and napalm bombs. No historical information has been located for the period of 1950-1976. Since 1976, the site has been used strictly as a non-hazardous solid waste landfill. A portion of the site was permitted as a sanitary landfill by the state of Ohio from 1978 until its closure in 1990. The landfill is regulated under RCRA while the remaining portion of the quarry is regulated under CERCLA.

Because this unit is unlined, there is potential for releases from the landfill to surrounding soils and groundwater. Five groundwater monitoring wells were installed around the landfill perimeter in 1988. The wells are monitored on a regular basis as part of the landfill closure requirements. New wells were installed in 1998 to further investigate the nature and extent of groundwater contamination at the landfill. A report of findings was published in October 1998. Low levels of explosives and metals have been detected in groundwater.

Additional wells were installed and soil, sediment and surface water samples were taken in fall 2003 to further determine the nature and extent of the contamination of the CERCLA portion of the quarry. A preliminary draft report on the findings is expected by winter 2004.

PROPOSED PLAN

Finalize reports. LTM will follow.

Note: Facility-wide groundwater monitoring will be partially funded under this site.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RI/FS

FUTURE IRP PHASE:

RI/FS, LTM

| Constr | Constrained Cost to Complete | | | | | |
|--------|-------------------------------------|------|------|-------|--|--|
| | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | |
| RI/FS | 156 | | 420 | | | |
| IRA | | | | | | |
| RD | | | | | | |
| RA | | | | | | |
| RA(O) | | | | | | |
| LTM | | | | 614 | | |
| | | | | | | |
| Total | 1,190,000 | | | | | |



Ravenna AAP - Installation Action Plan Site Descriptions - Page 2

RVAAP-02 ERIE BURNING GROUNDS

SITE DESCRIPTION

This 35 acre AOC was used to thermally treat munitions by open burning on the ground surface. Bulk, obsolete, off-spec propellants, conventional explosives, rags, and large explosive-contaminated items were treated at this location. The ash residue from the burns was left at the AOC. UXO is present at the site. Waste constituents of concern at this location include RDX, TNT, and heavy metals. There is a potential for release of contaminants from this unit to the surrounding soils, surface water/sediment and groundwater. This site is in a wetland area.

The PA/SI was completed in 1989. Phase I RI field work was conducted at this site in July 1999. The final report was completed in 2001. It was determined that additional groundwater sampling was needed.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals, SVOCs

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RI/FS

FUTURE IRP PHASE:

RI/FS, LTM

PROPOSED PLAN

Groundwater, soil and sediment samples will be taken in fall 2003. This report is expected in summer 2004.

| Constr | Constrained Cost to Complete | | | | | | |
|--------|-------------------------------------|------|------|-------|--|--|--|
| | | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | | |
| RI/FS | 16 | 122 | | | | | |
| IRA | | | | | | | |
| RD | | | | | | | |
| RA | | | | | | | |
| RA(O) | | | | | | | |
| LTM | | 35 | 30 | 30 | | | |
| | | | | | | | |
| Total | 233,000 | | | | | | |



Ravenna AAP - Installation Action Plan Site Descriptions - Page 3

RVAAP-04 OPEN DEMOLITION AREA #2

SITE DESCRIPTION

This AOC was used since 1948 to detonate large caliber munitions and off-spec bulk explosives that could not be deactivated or demilitarized by any other means due to their condition. Detonation was performed in a backhoe-dug pit with a minimum depth of 4 ft. After detonation, metal parts were picked up and removed from the site. The CERCLA (IRP) portion of the site is ~25 acres in size. Contaminants of concern at this site are white phosphorus, explosives, and heavy metals. Sand Creek bisects the site.

A Phase I RI was completed for the site in February 1998. The RI found explosives, particularly TNT, and several inorganics including cadmium, lead and mercury in both the surface and subsurface soils. Concentrations of inorganic compounds in sediment appear to be within site-wide background values. Groundwater is being investigated under the Phase II RI.

There is a smaller 1.5 acre area regulated under RCRA on the north side of Sand Creek, which was regularly used until 1992 for demolition activities. This area is not eligible for ER,A funding. A USAEHA geotechnical study was conducted at this site in 1992, with minor amounts of contamination being detected in the soils. Four groundwater monitoring wells were installed at the AOC as part of the USAEHA study. The wells are currently sampled on a quarterly basis. Low levels of explosives have been periodically detected in RCRA wells. Non-IRP funding was used in 1999 and 2000 to remove UXO/OE to a depth of 4 ft in the area of the 1.5 acre RCRA unit.

IRP funds are being used to characterize and properly handle any contaminated soils within the eligible areas.

In summer 2002, the Phase II RI field work was completed to better delineate the north side and delineate the south side of the AOC.

Work at this site is likely to be eligible for the Military Munitions Response Program (MMRP).

Facility-wide surface water and sediment sampling is being funded under this site, to evaluate the overall biological integrity of surface water by watershed.

PROPOSED PLAN

Prepare a RI report (draft expected in spring 2004). A RD/RA, such as fencing, bank stabilization and soil removal, may be required. LTM will follow.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI, Phase I RI (1998)

CURRENT IRP PHASE:

RI/FS

FUTURE IRP PHASE:

RI/FS (DD), RD, RA, LTM

| Constrained Cost to Complete | | | | | | | |
|-------------------------------------|-----------------|------|------|-------|--|--|--|
| | 2004 | 2005 | 2006 | 2007+ | | | |
| RI/FS | 145 | 100 | | | | | |
| IRA | | | | | | | |
| RD | | 18 | | | | | |
| RA | | | 1025 | 40 | | | |
| RA(O) | RA(O) | | | | | | |
| LTM | LTM 1659 | | | | | | |
| | | | | | | | |
| Total | 2,987,000 | | | | | | |

Aerial Photo of the Demolition Area #2.



Ravenna AAP - Installation Action Plan Site Descriptions - Page 4

RVAAP-05

WINKLEPECK BURNING GROUNDS

SITE DESCRIPTION

The total burning ground area consists of 200 acres and has been in operation since 1948. Prior to 1980, open burning was carried out in pits, pads, and sometimes on the roads within the 200 acre area. Burning was conducted on the bare ground and the ash was abandoned at the site. Prior to 1980, wastes treated in the area included RDX, antimony sulfide, Composition B, lead azide, TNT, propellants, black powder, waste oils, sludge from the load lines, domestic wastes and small amounts of laboratory chemicals. UXO is present at the AOC. From 1980 to 1998, burns of scrap explosives, propellants and explosive-contaminated materials were conducted in raised refractory-lined trays within a 1.5 acre area.

A USAEHA geotechnical study was conducted at the active portion of this site in 1992. The Part B permit application covering the active portion of the site was withdrawn in 1994. The burn trays along with the 90-day storage unit, Building 1601, were closed in accordance with Ohio EPA guidance in 1998. Minor amounts of contamination were detected in the soils.

Field work for a Phase II RI was conducted in 1998 and the report finalized in late 2002 (end use has since changed). The report includes facility-wide background levels, as well as human health and ecological risk assessments. Additional field studies were conducted in FY00 at Winklepeck and RVAAP reference locations to more accurately define the risk to ecological receptors at the site. The Draft Eco report was submitted in April 2001. This Eco report has undergone revisions and is currently undergoing finalization. Phase III RI fieldwork was completed in fall 2000, the preliminary draft report is expected to be submitted in late spring 2004. The data will be used along with data from previous studies to evaluate remedial alternatives.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals, SVOCs

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RI/FS, RD

FUTURE IRP PHASE:


RA, LTM

| Constrained Cost to Complete | | | | | |
|-------------------------------------|-----------|------|------|-------|--|
| | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | |
| RI/FS | 40 | | | | |
| IRA | | | | | |
| RD | 69 | | | | |
| RA | | 600 | 400 | | |
| RA(O) | | | | | |
| LTM | | | 760 | 240 | |
| | | | | | |
| Total | 2,109,000 | | | | |

PROPOSED PLAN

Finalize RI/FS reports. There will be some UXO removal in 2003-04 with non-IRP funds. A RD/RA, of soil removal in conjunction with UXO removal, is planned. LTM will follow.

The most likely future use of this site will be as an impact area for a training range for the Mk 19 grenade machine gun (target practice rounds only). This site has an increased priority for action in order to expedite property transfer to the National Guard Bureau.



RVAAP-06 C BLOCK QUARRY

SITE DESCRIPTION

This AOC is an abandoned borrow pit approximately 0.3 acres in size. The AOC was used as a disposal area for annealing process wastes (chromic acid) for a short time during the 1950s. Liquid wastes were apparently dumped on the ground in the pit bottom. The AOC is now heavily forested with trees of 1 ft diameter or larger. Waste constituents of concern include chromium, lead, and mercury.

A detailed sampling investigation of the soils from this unit in 1986 detected no metals above RCRA-regulated levels.

In the fall of 2001, additional samples were taken. Metals, including hexavalent chromium and organics were detected in soil above screening levels. The amount of contaminated soil is larger than previously expected. Groundwater has not been sampled.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Metals, Organics

MEDIA OF CONCERN:

Soil, Groundwater

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

None

FUTURE IRP PHASE:

RI/FS, RD, RA, LTM

PROPOSED PLAN

A RI/FS will be completed. Soil removal and LTM may be needed.

| Constr | Constrained Cost to Complete | | | | | | | |
|----------------|-------------------------------------|------|------|------|--|--|--|--|
| | 2004 2005 2006 2007+ | | | | | | | |
| DIVEO | 2004 | 2003 | 2000 | | | | | |
| RI/FS | | | | 965 | | | | |
| IRA | | | | | | | | |
| RD | | | | 33 | | | | |
| RA | | | | 1893 | | | | |
| RA(O) | | | | | | | | |
| LTM 454 | | | | | | | | |
| | | | | | | | | |
| Total | 3,345,000 | | | | | | | |



Ravenna AAP - Installation Action Plan Site Descriptions - Page 6

SITE DESCRIPTION

From approximately 1941 to 1971, wash-down water and wastewater from the load line operations were collected in concrete sumps, pumped through sawdust filtration units and then discharged to a settling pond. Building wash-down water from the melt-pour buildings was also swept out through doorways onto the ground surrounding the buildings. The settling pond was an unlined earthen impoundment ~1 acre in size. Water from the impoundment was discharged to a surface stream that exited the installation. This area was also used as a demil area. Contaminants of concern at this unit are explosive compounds and heavy metals (including lead, chromium, and mercury). There is a high potential for releases from this unit to the soils, surface water/sediment and groundwater. Most above ground structures were demolished during 2000. Environmental controls were used during the demolition activities to prevent migration of contaminants to the environment.

The RI sampling (1999-2000) found high levels of explosives in the soil around the melt-pour and preparation buildings. Groundwater has

STATUS

RRSE RATING: High CONTAMINANTS:

Explosives, Metals, SVOCs, VOCs

Propellents

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI, Phase I RI (1998), Phase II RI (2003)

CURRENT IRP PHASE:

PBC

FUTURE IRP PHASE:


PBC

low levels of explosives and metals. Preliminary screening of the contaminant levels indicates that the sediments may cause an ecological risk. Surface water did not shown any significant contamination. The RI report was finalized in June 2003.

PROPOSED PLAN

A PBC contract was awarded to Shaw Environmental in Sept 2003 to complete all phases through LTM at LL1, 2, 3 and 4 for all soils and some sediments.

Final: All concrete wall and foundations and walkways will be removed. Flushing and grouting or removal of the underground utilities will be done as needed. Any residual contamination will be removed. This may be accomplished with non-ER,A funds.

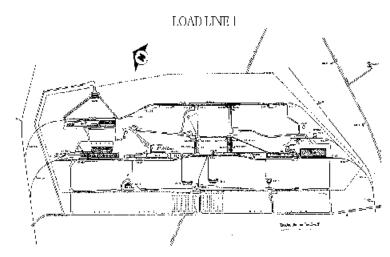

RVAAP-09 LOAD LINE 2

SITE DESCRIPTION

From approximately 1941 to 1971, building wash-down water and wastewater from the load line operations were collected in concrete sumps, pumped through sawdust filtration units and then discharged to a settling pond. Building wash-down water from the melt-pour buildings was also swept out through doorways onto the ground surrounding the buildings. The settling pond was an unlined triangular-shaped pond ~2 acres in size and 6 to 8 ft deep. Water from the impoundment was discharged to a surface stream that exited the installation. Contaminants of concern at this unit are explosive compounds and heavy metals (ex., lead, chromium, cadmium, and mercury). There is a high potential for releases from this unit to the soils, surface water/sediments and groundwater.

A Phase I RI was completed in 1998. Explosives and metals were the most common soil contaminants. Organics, PCBs, propellants and pesticides were also detected. Low levels of some contaminants were found in the groundwater at this site. Fieldwork for a Phase II RI to further determine the nature and extent of the contamination was completed in 2001. A preliminary draft of the findings was submitted in May 2003 with regulatory review completed in June 2003.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals, SVOCs, VOCs

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI, Phase I RI (1998)

CURRENT IRP PHASE:

PBC

FUTURE IRP PHASE:

PBC

Thermal decomposition of the building walls and foundations is being conducted (with non-ER,A funds).

PROPOSED PLAN

A PBC contract was awarded to Shaw Environmental in Sept 2003 to complete all phases through LTM at LL1, 2. 3 and 4 for all soils and some sediments.

Final: All concrete wall and foundations and walkways will be removed. Flushing and grouting or removal of the underground utilities will be done as needed. Any residual contamination will be removed. This may be accomplished with non-ER,A funds.



Ravenna AAP - Installation Action Plan Site Descriptions - Page 8

RVAAP-10 LOAD LINE 3

SITE DESCRIPTION

From approximately 1941 to 1971, building wash-down water and wastewater from the load line operations were collected in concrete sumps, pumped through sawdust filtration units and then discharged to a drainage ditch leading to a settling pond. Building wash-down water from the melt-pour buildings was also swept out through doorways onto the ground surrounding the buildings. Contaminants of concern at this unit are explosive compounds and heavy metals (ex., lead, chromium, and mercury). There is a high potential for releases from this unit to the soils, surface water/sediment and groundwater.

A Phase I RI was completed in 1998. Explosives and metals were the most common soil contaminants. Organics, PCBs, propellants and pesticides were also detected. Low levels of some contaminants were found in the groundwater at this site. Fieldwork for a Phase II RI to further determine the nature and extent of the contamination was completed in 2001. A preliminary draft RI report was submitted in May 2003 with regultory review completed in June 2003.

Thermal decomposition of the building walls and foundations will be conducted (with non-ER,A funds).

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals, SVOCs, VOCs

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI, Phase II RI (1998)

CURRENT IRP PHASE:

PBC

FUTURE IRP PHASE:


PBC

PROPOSED PLAN

A PBC contract was awarded to Shaw Environmental in Sept 2003 to complete all phases through LTM at LL1, 2, 3 and 4 for all soils and some sediments.

Final: All concrete wall and foundations and walkways will be removed. Flushing and grouting or removal of the underground utilities will be done as needed. Any residual contamination will be removed. This may be accomplished with non-ER,A funds.





RVAAP-11 LOAD LINE 4

SITE DESCRIPTION

From approximately 1943 to 1971, building wash-down water and waste water from the load line operations were collected in concrete sumps, pumped through sawdust filtration units and then discharged to a settling pond. Building wash-down water from the melt-pour buildings was also swept out through doorways onto the ground surrounding the buildings. The settling pond was an unlined triangular-shaped pond ~2 acres in size and 6 to 8 feet deep. Water from the impoundment was discharged to a surface stream that exited the installation. Contaminants of concern at this unit are explosive compounds and heavy metals (ex., lead, chromium, cadmium). There is a high potential for releases from this unit to the soils, surface water/ sediment and groundwater.

A Phase I RI was completed in 1998. Explosives and metals were the most common soil contaminants. Organics, PCBs, propellants and pesticides were also detected. Low levels of some contaminants were fround in the groundwater at this site. Fieldwork for a Phase II RI to further determine the nature and extent of the contamination was completed in 2001. A preliminary draft RI report was submitted in May 2003 with regulatory review completed in June 2003.

Thermal decomposition of the building walls and foundations will be conducted (with non-ER,A funds).

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Explosives, Metals, SVOCs, VOCs

MEDIA OF CONCERN:

 $Soil, Groundwater, Surface \, Water, \,$

Sediment

COMPLETED IRP PHASE:

PA/SI, Phase I RI (1998)

CURRENT IRP PHASE:

PBC


FUTURE IRP PHASE:

PBC

PROPOSED PLAN

A PBC contract was awarded to Shaw Environmental in Sept 2003 to complete all phases through LTM at LL1, 2, 3 and 4 for all soils and some sediments.

Final: All concrete wall and foundations and walkways will be removed. Flushing and grouting or removal of the underground utilities will be done as needed. Any residual contamination will be removed. This may be accomplished with non-ER,A funds.



RVAAP-12 LOAD LINE 12

SITE DESCRIPTION

From 1941-43 and 1946, ammonium nitrate was produced at this site. From 1949 to 1993, munitions were periodically demilitarized with building wash-down water and waste water from the bomb melt out facility operations being collected in a house gutter system, and flowing through a piping system to two stainless steel tanks. The first tank was used for settling and the second tank was used for filtration. Prior to the 1980s, the water leaked under the building and ponded there. Building wash-down water from Building 904 was also swept out through doorways onto the ground surrounding the building. After 1981, the water was treated in the Load Line 12 wastewater treatment system (RVAAP-18). Contaminants of concern at this unit are explosive compounds and heavy metals. There is a high potential for releases from this unit to the soils, surface water/sediment and groundwater. The original pink water treatment plant servicing Building 904 was officially closed as of May 2000.

A composting pilot study (IRA) using soils contaminated with explosives from the area of Building F-904 was started in 2000. The report from this pilot bioremediation project is final. Samples of environmental media were collected in the fall of 2000. The Phase II RI will be submitted in fall/winter 2003.

High levels of nitrates were detected in the groundwater. Metals and explosives were detected in the soil, sediment and groundwater. Metals were detected in surface water.

The Phase II RI report is being reviewed by regulators.

PROPOSED PLAN

Finalize the RI report. A FS will be completed. Additional soil removal is likely to be required.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI, Phase I RI (1998), IRA


CURRENT IRP PHASE:

RI

FUTURE IRP PHASE:

FS, RD, RA, LTM

| Constrained Cost to Complete | | | | | |
|-------------------------------------|-----------|------|------|-------|--|
| | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | |
| RI/FS | 239 | 50 | | | |
| IRA | | | | | |
| RD | | | 5 | | |
| RA | | | | 213 | |
| RA(O) | | | | 922 | |
| LTM | | | | | |
| | | | | | |
| Total | 1,429,000 | | | | |

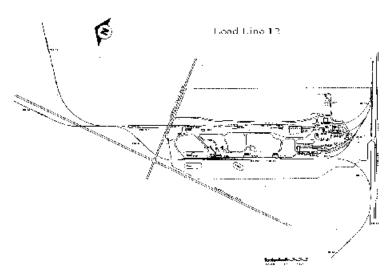

RVAAP-13

BUILDING 1200 DILUTION/SETTLING POND

SITE DESCRIPTION

From approximately 1941 to 1971, ammunition was demilled at this building by steaming munitions rounds. The steam decontamination generated pink water, which drained to a man-made ditch. The ditch discharged into a 0.5-acre sedimentation pond, and the overflow from this pond discharged into Sand Creek. Contaminants of concern at this unit are explosive compounds and heavy metals (including lead, chromium, and mercury). There is a potential for releases from this unit to the soils, surface water/sediment and groundwater.

Limited explosives and metals contamination was detected in the ditch and settling ponds during the Phase I RI.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI, Phase I RI (1998)

CURRENT IRP PHASE:

None

FUTURE IRP PHASE:

RI/FS, RD, RA, LTM

PROPOSED PLAN

A RI/FS will be completed. Soil removal is expected. LTM will follow.

| Constr | Constrained Cost to Complete | | | | | | | |
|--------|-------------------------------------|------|------|-------|--|--|--|--|
| | 2004 2005 2006 2007+ | | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | | | |
| RI/FS | | | | 686 | | | | |
| IRA | | | | | | | | |
| RD | | | | 5 | | | | |
| RA | | | | 213 | | | | |
| RA(O) | | | | | | | | |
| LTM | | | | 400 | | | | |
| | | | | | | | | |
| Total | 1,304,000 | | | | | | | |



Ravenna AAP - Installation Action Plan Site Descriptions - Page 12

RVAAP-16

FUZE AND BOOSTER QUARRY LANDFILL/PONDS

SITE DESCRIPTION

This AOC operated during the period 1945 through 1993. The site consists of three ponds in an abandoned rock quarry. The ponds are 20 to 30 ft deep and are separated by earthen berms. Prior to 1976, the quarry was reportedly used for open burning and as a landfill. The debris from the burning/landfill was reported to have been removed during pond construction. From 1976-93, spent brine regenerate and sand filtration backwash water from one of the RVAAP drinking water treatment plants was discharged into the ponds. This discharge was regulated under a NPDES permit. In 1998, this AOC was expanded to include three other shallow settling ponds and two debris piles, bringing the site to ~45 acres. The lands adjacent to the quarry were utilized as an impact area to test 40mm projectiles and to incinerate/deactivate fuze and booster components.

Constituents of concern include explosive compounds and heavy metals. There is a potential for release of contaminants to the groundwater, soils and surface water/sediment from this AOC.

The Phase II RI field work was completed in November 2003.

PROPOSED PLAN

 \mbox{RI} work will be required. A RD/RA of sediment and/or debris removal may be needed.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI (1989)

CURRENT IRP PHASE:

R

FUTURE IRP PHASE:

RI/FS, RD, RA, LTM

| Constrained Cost to Complete | | | | | | |
|-------------------------------------|----------------------|-----|-----|--------|--|--|
| | 2004 2005 2006 2007+ | | | | | |
| | | | | 2007 T | | |
| RI/FS | 487 | 540 | 120 | | | |
| IRA | | | | | | |
| RD | | | | 15 | | |
| RA | | | | 566 | | |
| RA(O) | | | | 435 | | |
| LTM | | | | | | |
| | | | | | | |
| Total | 2,163,000 | | | | | |



ivenna AAP - Installation Action Plan Site Descriptions - Page 13

RVAAP-19 LANDFILL NORTH OF WINKLEPECK BURNING GROUNDS

SITE DESCRIPTION

This is a 10 acre unlined landfill used for general plant refuse (sanitary wastes, possibly also explosive wastes and ash residue). It was used from 1969 until 1976 and has minimum soil cover. This landfill is upgradient of a wetland area.

The Phase I RI sampling and trenching were completed in 1996. Low levels of metals (above background), pesticides, PCBs and SVOCs, were detected in soil. Low levels of metals were detected in sediment.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Metals, SVOCs, Pesticides, PCBs

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI, Phase I RI (1998)

CURRENT IRP PHASE:

None

FUTURE IRP PHASE:

RI/FS, RD, RA, RA(O), LTM

PROPOSED PLAN

Soil and groundwater samples will be taken. Limited soil cover may be needed, followed by LTM.

| Constrained Cost to Complete | | | | | | |
|------------------------------|-----------|------|------|-------|--|--|
| | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | |
| RI/FS | | | | 611 | | |
| IRA | | | | | | |
| RD | | | | 41 | | |
| RA | | | | 988 | | |
| RA(O) | | | | 66 | | |
| LTM | | | | 210 | | |
| | | | | | | |
| Total | 1,916,000 | | | | | |



MUSTARD AGENT BURIAL SITE

SITE DESCRIPTION

This unit is a possible mustard agent burial site ~15 x 18 ft and is triangularly shaped. In 1969, records indicate that an EOD Unit had excavated a suspected mustard agent burial site near the west end of the NACA runway. One 190 liter (50 gallon) drum and seven rusty canisters were recovered. All recovered items were empty and no contamination was discovered. Following this excavation, an unidentified and undocumented source reported that the site had not been correctly identified and was actually in an adjacent area.

This additional area (\sim 15 x 18 ft) is located southwest of the original area. The area in now marked by Seibert (reflective) stakes. Two non-intrusive, geophysical surveys (EM-31, and EM-61) of the site were completed in 1998. Several areas were identified with metallic responses. Some, if not all, may be related to cultural features at or near the surface. Soil samples taken in 1998 found no thiodiglycol (mustard breakdown product). There was no sign of disturbed soils or numerous buried metallic objects that would clearly delineate a formal burial site.

PROPOSED PLAN

Groundwater samples will be collected to test for mustard breakdown products.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Mustard Agent

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water

COMPLETED IRP PHASE:

PA/SI, Phase I RI (1998)

CURRENT IRP PHASE:

RI/FS

FUTURE IRP PHASE:

RC

| Constrained Cost to Complete | | | | | | |
|-------------------------------------|---------|------|------|-------|--|--|
| | - | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | |
| RI/FS | 162 | | | | | |
| IRA | | | | | | |
| RD | | | | | | |
| RA | | | | | | |
| RA(O) | | | | | | |
| LTM | | | | | | |
| • • • | | | | | | |
| Total | 162,000 | | | | | |



RVAAP-29

UPPER & LOWER COBB PONDS

SITE DESCRIPTION

The Upper and Lower Cobb Pond complex consists of two unlined ponds that received discharges from Load Lines 3 and 12 explosive waste water treatment systems from 1941 through 1971. Upper Cobb Pond is ~5 acres in size and Lower Cobb Pond is ~4 acres in size.

The Phase I RI found low levels of explosives in sediment; no contaminants were found in the surface water. The Phase II RI field work was completed in the summer 2001. Soil, sediment, surface water and groundwater were sampled. The Preliminary Draft Report is expected to be submitted in spring 2004.

This site is partially addressed under the Facility-Wide Surface Water sampling program.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Explosives, Metals, Aluminum Chloride

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI, Phase I RI (1998)

CURRENT IRP PHASE:

RI/FS

FUTURE IRP PHASE:

RI/FS, LTM

PROPOSED PLAN

Prepare and submit the RI report. No remedial action is expected. LTM may follow.

| Constrained Cost to Complete | | | | | | | |
|-------------------------------------|-----------|------|------|-------|--|--|--|
| | | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | | |
| RI/FS | 49 | 204 | | | | | |
| IRA | | | | | | | |
| RD | | | | | | | |
| RA | | | | | | | |
| RA(O) | | | | | | | |
| LTM | | | 609 | 150 | | | |
| | | | | | | | |
| Total | 1,012,000 | | | | | | |



Ravenna AAP - Installation Action Plan Site Descriptions - Page 16

40 AND 60 MM FIRING RANGE

SITE DESCRIPTION

This site was used as a test firing range for 40 mm projectiles during the late 1960s and early 1970s. This AOC was reported by former workers at RVAAP to have been a test firing range for munitions. The dates of this operation were from 1969-71. No original file documentation exists for the operation. UXO is suspected at this ~2-acre site.

The site is now covered with pole timber. Soil samples collected by CHPPM in 1996, detected arsenic and cadmium above the RRSE screening concentrations.

Additional samples were taken in fall 2003.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Metals

MEDIA OF CONCERN:

Soil

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RI/FS


FUTURE IRP PHASE:

RI/FS

PROPOSED PLAN

RI sampling, including UXO precautions, will be completed.

| Constrained Cost to Complete | | | | | | | |
|-------------------------------------|---------|------|------|-------|--|--|--|
| | | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | | |
| RI/FS | 20 | | | 314 | | | |
| IRA | | | | | | | |
| RD | | | | | | | |
| RA | | | | | | | |
| RA(O) | | | | | | | |
| LTM | | | | | | | |
| | | | | | | | |
| Total | 334,000 | | | | | | |

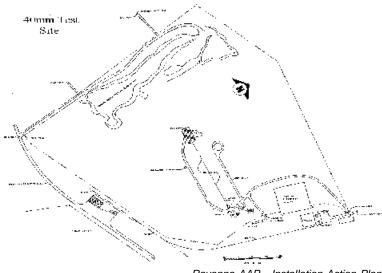

RVAAP-33 LOAD LINE 6

SITE DESCRIPTION

This unit, also known as the Firestone Test Facility, was reported by former workers at RVAAP to have been a security classified experimental test facility for munitions. Shaped charges were constructed and tested for the Department of Defense. The site consists of a pond (underwater test chamber) and several buildings (~45 acres). The dates of operation are not known. No original file documentation exists for this site. The contaminants of potential concern are lead azide, TNT, RDX, other explosives and metals.

Soil samples collected by CHPPM in 1996, detected antimony, copper and lead above the RRSE screening concentrations. The buildings were thermally treated and the remaining structures removed in 2003. THe Phase I RI field work was completed in November 2003.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Lead Azide, Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RI/FS

FUTURE IRP PHASE:

RI/FS, RD, RA, LTM

PROPOSED PLAN

A RI will be completed. A RD/RA, such as soil removal may be needed.

All foundations and footers (to 4 ft bgs) will be removed. Flushing and grouting or removal of the underground utilities will be done as needed. Any residual contamination will be removed. This will be accomplished with non-ER,A funds.

| Constrained Cost to Complete | | | | | | | |
|-------------------------------------|-----------|------|------|-------|--|--|--|
| | | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | | |
| RI/FS | 136 | 40 | 40 | 100 | | | |
| IRA | | | | | | | |
| RD | | | | 17 | | | |
| RA | | | | 747 | | | |
| RA(O) | | | | | | | |
| LTM | | | | 769 | | | |
| | | | | | | | |
| Total | 1,849,000 | | | | | | |



RVAAP-34

SAND CREEK DISPOSAL ROAD LANDFILL

SITE DESCRIPTION

This AOC was reported by former workers at RVAAP to have been an open dump for concrete, wood, asbestos debris, lab bottles, 55-gallon drums and fluorescent light tubes. Debris is at the surface, but covered by vegetation. The AOC is ~2.7 acres and located adjacent to Sand Creek. The dates of operation of this unit are not known, but are believed to be around the 1950s. No original file documentation exists. The debris is eroding into Sand Creek.

Arsenic was detected in sediment at levels above the RRSE screening concentrations. Soil samples were taken by the USACE in September 2001 to further refine the RRSE. Arsenic (87ppm), benzo(a)pyrene (0.322ppm), benzo(a)athracene (0.347ppm), benzo(b)fluoranthene (0.446ppm) and indeno(1,2,3-cd)pyrene were detected at significant concentrations. The high RRSE rating was confirmed by this sampling event.

Soil and debris removal (IRA) was completed in summer 2003. The preliminary report is expected in early spring 2004.

PROPOSED PLAN

Complete the IRA report. Additional soil/debris removal may be needed (possibly addressed with non-ER,A funds).

STATUS

RRSE RATING:

High

CONTAMINANTS:

Heavy Metals, Asbestos, PAHs

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RI/FS

FUTURE IRP PHASE:

RC

| Constrained Cost to Complete | | | | | | |
|-------------------------------------|--------|------|------|-------|--|--|
| | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | |
| RI/FS | 60 | | | | | |
| IRA | | | | | | |
| RD | | | | | | |
| RA | | | | | | |
| RA(O) | | | | | | |
| LTM | | | | | | |
| | | | | | | |
| Total | 60,000 | | | | | |



RVAAP-36 PISTOL RANGE

SITE DESCRIPTION

This AOC was used by the installation security force for pistol qualification. Bullets were fired into the embankment. The unit size is 350×150 ft. No original file documentation exists for this site.

CHPPM samples detected lead in the soil at a maximum concentration of 4,309 ppm.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Lead

MEDIA OF CONCERN:

Soil, Surface Water, Sediment

COMPLETED IRP PHASE:

PA/SI, RI/FS

CURRENT IRP PHASE:

RD

FUTURE IRP PHASE:

RA

PROPOSED PLAN

RD and RA will include the removal and sifting of the top foot of soil, followed by lime stabilization and return of the sifted soil. The site will be seeded and mulched.

| Constrained Cost to Complete | | | | | | | |
|-------------------------------------|---------|------|------|-------|--|--|--|
| | | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | | |
| RI/FS | | | | | | | |
| IRA | | | | | | | |
| RD | 22 | | | | | | |
| RA | | 388 | | | | | |
| RA(O) | (O) | | | | | | |
| LTM | | | | | | | |
| | | | | | | | |
| Total | 410,000 | | | | | | |



RVAAP-38 NACA TEST AREA

SITE DESCRIPTION

This is an approximately 12.4 acre AOC that was used as an aircraft test area. Surplus military aircraft were crashed into a barrier using a fixed rail attached to the aircraft landing gear in an attempt to develop crashworthy fuel tanks and/or high flashpoint fuel. Some of the aircraft were buried at the site after the tests. Demo Area #1, RVAAP-03, is located within the RVAAP-38 boundary.

Phase I RI samples were taken in October 1999. The Phase I RI was completed in 2000 and finalized in fall 2001. Low levels of metals, inorganics and VOCs were detected in soil. Nitrocellulose was detected in the sediment, but is believed to be attributed to RVAAP-03.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Metals, Inorganics, VOCs

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI, Phase I RI

CURRENT IRP PHASE:

Vone

FUTURE IRP PHASE:

Phase II RI/FS, RD, RA, LTM

PROPOSED PLAN

Additional RI work will be completed. This will include installing monitoring wells, that will be used to monitor this site and RVAAP-03. Evaluate risk. Soil bioremediation may be used over part of the site, followed by LTM.

| Constrained Cost to Complete | | | | | |
|-------------------------------------|----------------------|-----|----|-----|--|
| | 2004 2005 2006 2007+ | | | | |
| RI/FS | | 128 | 17 | 332 | |
| IRA | | | | | |
| RD | | | | 24 | |
| RA | | | | 237 | |
| RA(O) | | | | 564 | |
| LTM | | | | | |
| Total 1.302.000 | | | | | |



Ravenna AAP - Installation Action Plan Site Descriptions - Page 21

RVAAP-39 LOAD LINE 5

SITE DESCRIPTION

This AOC was a load line that was operated from 1941 to 1945 to produce fuzes for artillery projectiles. Load line 5 was deactivated and its equipment removed in 1945.

The relative risk site evaluation was completed in 1998 by USACHPPM. The surface soil and groundwater pathways are considered complete. Six surface soil samples were collected from outside of the production buildings and analyzed for explosives and metals. The sampling locations were selected based on the production use. Emphasis was placed on those buildings that were used to load the black powder and mercury fulminate. One sediment sample was originally going to be collected from one of the settling ponds at the AOC, but no settling ponds or other sediment pathways were evident. Surface soils were found to have a maximum lead concentration of 2,800 ppm. Explosives were not detected in any samples taken by USACHPPM.

Screening groundwater data collected for RVAAP-26, Fuze and Booster Area Settling Tanks during the first RRSE, was used to score the groundwater pathway at the AOC. Groundwater was collected from an approximate depth of 12 ft adjacent to the settling tank next to Building 1F-3.

PROPOSED PLAN

A RI will be completed. Thermal treatment of buildings will be conducted. A RD/RA such as soil removal may be needed.

All foundations and footers (to 4 ft bgs) will be removed. Flushing and grouting or removal of the underground utilities will be done as needed. Any residual contamination will be removed. This will be accomplished with non-ER,A funds.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:


PA/SI

CURRENT IRP PHASE:

None

FUTURE IRP PHASE:

| Constr | Constrained Cost to Complete | | | |
|--------|-------------------------------------|------|------|-------|
| | | | | 1 |
| | 2004 | 2005 | 2006 | 2007+ |
| RI/FS | | | | 1157 |
| IRA | | | | |
| RD | | | | 8 |
| RA | | | | 258 |
| RA(O) | | | | |
| LTM | | | | 369 |
| | | | | |
| Total | 1,792,000 | | | |

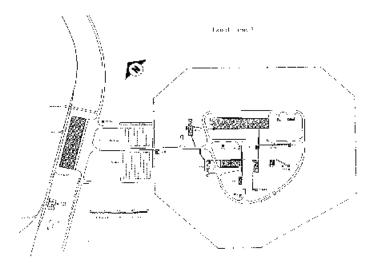

RVAAP-40 LOAD LINE 7

SITE DESCRIPTION

This AOC was used to assemble booster charges for artillery projectiles between 1941 and 1945. Load Line 7 was deactivated and the equipment was removed in 1945. The LL-7 was used again in 1969 and 1970 to produce 40mm projectiles, and between 1989 and 1993 the LL-7 Pink Water Treatment Plant was in operation.

The relative risk site evaluation was completed in 1998 by USACHPPM. The surface soil and groundwater pathways are considered complete. Six surface soil samples were collected from outside of the production buildings and analyzed for explosives and metals. The sampling locations were selected based on the production use. Emphasis was placed on areas around production and explosive storage buildings. One sediment sample was originally going to be collected from one of the settling ponds at the AOC, but no settling ponds or other sediment pathways were evident. One screening groundwater sample was collected north-northwest of Building 1B-2 (down gradient by surface topography) and analyzed for explosives and metals. The groundwater was collected from between 8 and 9 feet bgs. Significant concentrations of lead (maximum 2,000 ppm) and low concentrations of explosives, HMX, RDX and 2,4,6 TNT, were found in the surface soils.

PROPOSED PLAN

A RI will be completed. Thermal treatment of buildings will be conducted. A RD and RA, such as soil removal, may be needed.

All foundations and footers (to 4 ft bgs) will be removed. Flushing and grouting or removal of the underground utilities will be done as needed. Any residual contamination will be removed. This will be accomplished with non-ER,A funds.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:


PA/SI

CURRENT IRP PHASE:

None

FUTURE IRP PHASE:

| Constrained Cost to Complete | | | | | | |
|-------------------------------------|------|----------------------|-------|------|--|--|
| | 2004 | 2004 2005 2006 2007+ | | | | |
| RI/FS | | | | 1157 | | |
| IRA | | | | | | |
| RD | | | | 8 | | |
| RA | | | | 258 | | |
| RA(O) | | | | | | |
| LTM | | | | 369 | | |
| T 1 1 1 200 000 | | | | | | |
| Total | | 1,79 | 2,000 | | | |

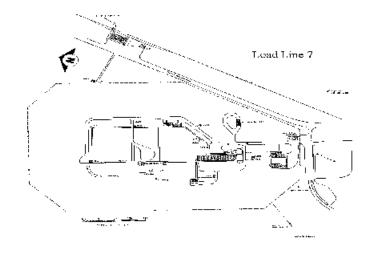

RVAAP-41 LOAD LINE 8

SITE DESCRIPTION

This AOC was used to assemble booster charges for artillery projectiles between 1941 and 1945. Load Line 8 was deactivated and the equipment was removed in 1945.

The relative risk site evaluation was completed in 1998 by USACHPPM. The surface soil, groundwater and sediment pathways are considered complete. Five surface soil samples and one groundwater sample were collected from outside of the assembly buildings and analyzed for explosives and metals. The sampling locations were selected based on assembly use. Sample point selection emphasized production and explosives storage buildings. One sediment sample was collected from the small (approximately 10 feet in diameter) settling pond at the AOC and analyzed for the same compounds. No surface water was collected from the settling pond since this would be an intermittent source, and is not significant for the purpose of the RRSE. The subsurface soil used to estimate the groundwater pathway was collected approximately 60 feet northnorthwest of Building 2B-1 (downgradient by surface topography). Lead was found in the surface soil at a maximum concentration of 1,000 ppm. No explosives were detected.

PROPOSED PLAN

A RI will be completed. Thermal treatment of buildings will be conducted. A RD and RA, such as soil removal, may be needed.

All foundations and footers (to 4 ft bgs) will be removed. Flushing and grouting or removal of the underground utilities will be done as needed. Any residual contamination will be removed. This will be accomplished with non-ER,A funds.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:


PA/SI

CURRENT IRP PHASE:

None

FUTURE IRP PHASE:

| Constrained Cost to Complete | | | | | | | |
|-------------------------------------|---------|----------------------|-----|-----|--|--|--|
| | 2004 | 2004 2005 2006 2007+ | | | | | |
| RI/FS | | | 502 | 655 | | | |
| IRA | | | | | | | |
| RD | | | | 8 | | | |
| RA | | | | 258 | | | |
| RA(O) | | | | | | | |
| LTM | LTM 369 | | | | | | |
| | | | | | | | |
| Total | | 1,792,000 | | | | | |

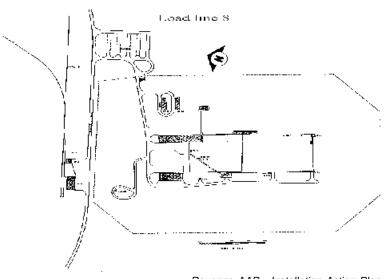

RVAAP-42 LOAD LINE 9

SITE DESCRIPTION

This AOC operated from 1941 to 1945 to produce detonators. Load Line 9 was deactivated and its equipment removed in 1945.

The relative risk site evaluation was completed in 1998 by USACHPPM. The surface soil and groundwater pathways are considered complete. Six surface soil samples were collected from outside of the production buildings and analyzed for explosives and metals. The sampling locations were selected based on the production use. Emphasis was placed on the buildings that were used to process and store the lead azide and tetryl. One sediment sample was originally going to be collected from one of the settling ponds at the AOC, but no settling ponds or other sediment pathways were evident. Subsurface soil data collected for RVAAP-26, Fuze and Booster Area Settling Tanks during the first RRSE, was used to score the groundwater pathway at the AOC. The subsurface soil used to estimate the groundwater pathway was collected adjacent to the settling tank on the east side of Building DT-5. Lead was the only contaminant that exceeded the RRSE standard concentration in the surface soil. No explosives were detected during the RRSE sampling.

Limited samples taken in 2000 detected low levels (below 2%) of lead azide in sediment and surface water in the sumps. The buildings were thermally treated and the remaining structures removed in 2003. The Phase I RI field work was completed in November 2003.

PROPOSED PLAN

Complete RI. A RD and RA, such as soil removal, may be needed.

All foundations and footers (to 4 ft bgs) will be removed. Flushing and grouting or removal of the underground utilities will be done as needed. Any residual contamination will be removed. This will be accomplished with non-ER,A funds.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:


PA/SI

CURRENT IRP PHASE:

RI/FS

FUTURE IRP PHASE:

| Constrained Cost to Complete | | | | | |
|-------------------------------------|------|------|-------|-------|--|
| | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | |
| RI/FS | 118 | 83 | | | |
| IRA | | | | | |
| RD | | | 8 | | |
| RA | | | | 258 | |
| RA(O) | | | | | |
| LTM | | | | 297 | |
| | | | | | |
| Total | | 764 | l,000 | | |

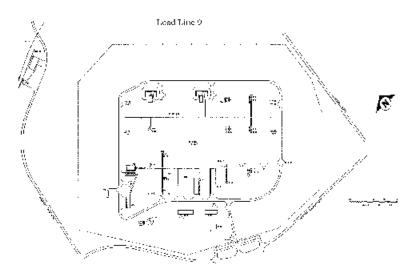

RVAAP-43 LOAD LINE 10

SITE DESCRIPTION

This AOC operated from 1941 to 1945 to produce percussion elements. Load Line 10 was placed on standby in 1945. From 1951 to 1957, LL-10 produced primers and percussion elements. From 1969 to 1971, LL-10 was used again to produce primers. It has been inactive since.

The relative risk site evaluation was completed in 1998 by USACHPPM. The surface soil and groundwater pathways are considered complete. Six surface soil samples were collected from outside of the production buildings and analyzed for explosives, metals and cyanide. The sampling locations were selected based on the production use. Emphasis was placed on those buildings that were used to produce or store the explosives. LL10 is the only load line known to have lead thiocyanate, so cyanide was added to the list of analytes. One sediment sample was originally going to be collected from one of the settling ponds at the AOC, but no settling ponds or other sediment pathway were evident. Antimony (maximum 600 ppm) and lead (maximum 3,100 ppm) were detected in the surface soil at levels above the RRSE standard concentrations. Small amounts of explosives (2,4,6 TNT, 4am 2,6 DNT and 2am 4,6 DNT) were detected in the surface soil. Subsurface soil data collected for RVAAP-26, Fuze and Booster Area Settling Tanks during the first RRSE, was used to score the groundwater pathway at the AOC. The subsurface soil used to estimate the groundwater pathway was collected adjacent to the settling tank on the west site of Bldg PE-6.

PROPOSED PLAN

A RI will be completed. Thermal treatment of buildings will be conducted. A RD and RA, such as soil removal, may be needed.

All foundations and footers (to 4 ft bgs) will be removed. Flushing and grouting or removal of the underground utilities will be done as needed. Any residual contamination will be removed. This will be accomplished with non-

ER, A funds.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater

COMPLETED IRP PHASE:


PA/SI

CURRENT IRP PHASE:

None

FUTURE IRP PHASE:

| Constrained Cost to Complete | | | | | |
|------------------------------|-----------|------|------|-------|--|
| | 2004 | 2005 | 2006 | 2007+ | |
| RI/FS | | | | 1229 | |
| IRA | | | | | |
| RD | | | | 8 | |
| RA | | | | 258 | |
| RA(O) | | | | | |
| LTM | TM 297 | | | | |
| | | | | | |
| Total | 1,792,000 | | | | |

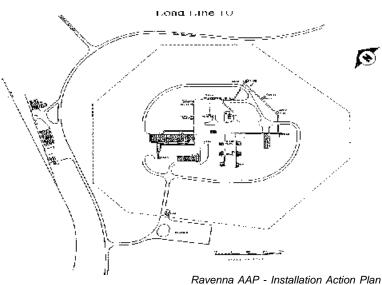

RVAAP-44 LOAD LINE 11

SITE DESCRIPTION

This AOC operated from 1941 to 1945 to produce primers for artillery projectiles. Load Line 11 was placed on standby in 1945. From 1951 to 1957, LL-11 was used to produce primers and fuzes.

The relative risk site evaluation was completed in 1998 by USACHPPM. The surface soil, groundwater and sediment pathways are considered complete. Five surface soil samples were collected from outside of the production buildings and analyzed for explosives and metals. The sampling locations were selected based on the production use. Emphasis was placed on those buildings that were used to produce and store explosives. One sediment sample was collected and analyzed for the same parameters. The sediment sample was collected from a drainage ditch running north from the load line. Data collected for RVAAP-26, Fuze and Booster Area Settling Tanks during the first RRSE, was used to score the groundwater pathway at the AOC. The subsurface soil used to estimate the groundwater pathway was collected adjacent to the settling tank immediately to the east of Building AP-3. Arsenic was detected in the sediment slightly above the RRSE ecological screening concentration. Lead was the only contaminant found in the surface soil with a maximum concentration of 11,000ppm.

In 2001, the lead-lined sumps, lead contaminated sediments, and solvent contaminated soils were removed during an IRA in 2001. Some of the sewer lines were also permannetly plugged with grout to prevent migration of contaminants. The RI field work was conducted in FY01.

Note: No perchlorate was detected in groundwater. The detection limit was 4 ppb.

PROPOSED PLAN

Prepare the RI report. Thermal treatment of buildings will be conducted. No remediation is expected. LTM will follow.

All foundations and footers (to 4 ft bgs) will be removed. Flushing and grouting or removal of the underground utilities will be done as needed. Any residual contamination will be removed. This will be accomplished with non-ER,A funds.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals, VOCs

MEDIA OF CONCERN:

Soil, Groundwater, Sediment

COMPLETED IRP PHASE:

PA/SI


CURRENT IRP PHASE:

RI/FS

FUTURE IRP PHASE:

LTM

| Constrained Cost to Complete | | | | | | |
|-------------------------------------|----------------------|------|------|-------|--|--|
| | 2004 2005 2006 2007+ | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | |
| RI/FS | 40 | | | | | |
| IRA | | | | | | |
| RD | | | | | | |
| RA | | | | | | |
| RA(O) | | | | | | |
| LTM | 449 100 | | | | | |
| | | | | | | |
| Total | | 589 | ,000 | | | |

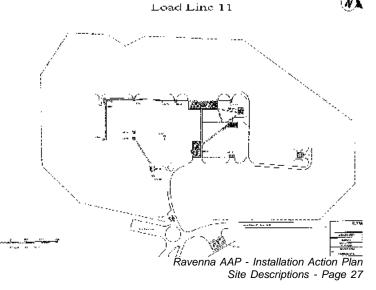

RVAAP-45 WET STORAGE AREA

SITE DESCRIPTION

This AOC was used from 1941 to 1945 to store (in igloos) lead azide, mercury fulminate and tetryl. The product was stored in water-filled drums. There is no documentation concerning any spills in the area. The surface soil pathway is considered complete.

Five surface soil samples were collected from the AOC and analyzed for explosives and metals. One sample was collected outside the door, just off of the edge of the concrete pad from each of the five buildings used for storage, or from the soil immediately below a discharge from a floor drain. The most significant contaminant concentrations were from lead (3,100ppm), mercury (49ppm) and cadmium (41ppm).

The buildings were thermally treated in spring 2003.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Metals, Lead Azide, Mercury Fulmate,

Tetryl

MEDIA OF CONCERN:

Soil

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

None

FUTURE IRP PHASE:


RI/FS, LTM

PROPOSED PLAN

The demolition of the structures is expected to be completed by Dec 2003.

Complete a RI. Only limited action is expected once a full and representative sampling program is completed.

| Constr | Constrained Cost to Complete | | | | | |
|--------|-------------------------------------|------|------|-------|--|--|
| | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | |
| RI/FS | | | | 359 | | |
| IRA | | | | | | |
| RD | | | | | | |
| RA | | | | | | |
| RA(O) | | | | | | |
| LTM | | | | 120 | | |
| | | | | | | |
| Total | 479,000 | | | | | |

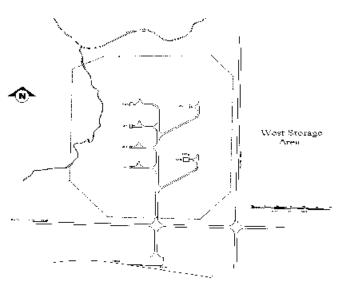

RVAAP-46 BLDG F-15 & F-16

SITE DESCRIPTION

These buildings were used during World War II, the Korean Conflict and Vietnam War to test miscellaneous explosives. Quantities and exact dates of testing are unknown.

The surface soil and sediment pathways are considered completed at this AOC. Four surface soil samples were collected from the AOC and analyzed for explosives and metals. Two samples were collected just outside of the foundations of each of the buildings. One sediment sample was collected in a drainage ditch leading to Sand Creek near Building F-16. Soil samples showed slightly elevated levels of lead (maximum 430 ppm) and arsenic (maximum 28 ppm). Arsenic was also detected in the sediment at a maximum concentration of 9 ppm, approximately 1.5 times the ecological RRSE screening concentration.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Sediment

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RI/FS

FUTURE IRP PHASE:

RI/FS, RD, RA

PROPOSED PLAN

A RI will be completed. Limited sediment removal may be required.

| Constrained Cost to Complete | | | | | | |
|------------------------------|---------|----------------------|-----|-----|--|--|
| | 2004 | 2004 2005 2006 2007+ | | | | |
| RI/FS | 51 | 161 | 147 | | | |
| IRA | | | | | | |
| RD | | | | 34 | | |
| RA | | _ | | 474 | | |
| RA(O) | | | | | | |
| LTM | | _ | | | | |
| | | | | | | |
| Total | 867,000 | | | | | |



RVAAP-48 ANCHOR TEST AREA

SITE DESCRIPTION

Limited information is known about this research and development area. It is believed that the site was used for testing of explosively driven soil anchoring devices. The dates of use for this AOC are unknown. It currently consists of several dirt mounds with a nearby sand pit (~6 x 30ft). There is some metal debris in the area.

The surface soil and groundwater pathways are considered complete. Five soil samples and one Geoprobe groundwater sample were collected from around the dirt mound and in the sand pit. These were analyzed for metals and explosives as part of the USACHPPM study. Arsenic was detected in the groundwater at a maximum concentration of 14.4 ppb; arsenic was also detected in the soil.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Sediment

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

None


FUTURE IRP PHASE:

RI/FS, LTM

PROPOSED PLAN

Limited soil sampling is planned. No remediation is expected. LTM may follow.

| Constrained Cost to Complete | | | | | | |
|-------------------------------------|------|----------------------|--|------|--|--|
| | 2004 | 2004 2005 2006 2007+ | | | | |
| RI/FS | | | | 284 | | |
| IRA | | | | | | |
| RD | | | | | | |
| RA | | | | | | |
| RA(O) | | | | | | |
| LTM | | | | 1137 | | |
| | | | | | | |
| Total | | 1.421.000 | | | | |

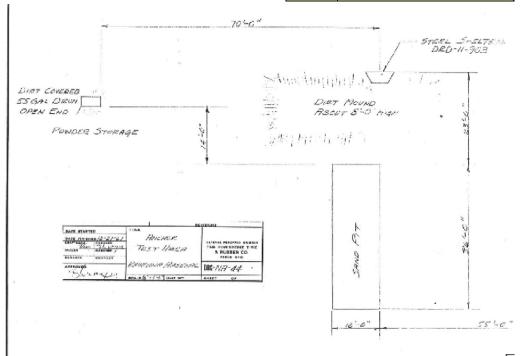

Ravenna AAP - Installation Action Plan Site Descriptions - Page 30

RVAAP-49 CENTRAL BURN PITS

SITE DESCRIPTION

This approximately 20 acre AOC was used for the burning of non-explosive scrap materials. The dates of operation for the AOC are unknown.

The surface soil and groundwater pathways are considered complete. Five surface soil samples were collected and analyzed for SVOCs, PCBs, herbicides, explosives and metals. One subsurface soil sample was collected and analyzed for the same compounds plus VOCs. The subsurface soil used to estimate the groundwater pathway was collected from the eastern limit (downhill side) of the main disturbed area. The USACHPPM sampling detected significant levels of antimony (maximum 9,000 ppm), arsenic (maximum 30 ppm) and lead (maximum 2,200 ppm) in the soil.

Field work for the Phase I RI was done in summer 2001; the report is pending.

PROPOSED PLAN

The Phase I RI will be completed (preliminary draft is expected in spring 2004). A FS will be completed. A RD/RA of soil removal may be required, followed by LTM.

STATUS

RRSE RATING:

High

CONTAMINANTS:

VOCs, SVOCs,PCBs, Herbicides, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water, Sediment

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RI/FS

FUTURE IRP PHASE:

| Constrained Cost to Complete | | | | | |
|-------------------------------------|------|------|-------|-------|--|
| | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | |
| RI/FS | 284 | 120 | | | |
| IRA | | | | | |
| RD | | | 16 | | |
| RA | | | 804 | | |
| RA(O) | | | | | |
| LTM | 702 | | | | |
| | | | | | |
| Total | | 1,92 | 6,000 | | |



RVAAP-50 ATLAS SCRAP YARD

SITE DESCRIPTION

This AOC is the site of an old construction camp (approximately 150 acres) built to house workers during the construction of the plant. Facilities were demolished following World War II. Since that time, the area has been used as a scrap yard for miscellaneous materials. UXO is present at the southwest corner of the site.

Preliminary samples detected low levels of PAHs in soil and metals in one screening groundwater sample.

Non-IRP sorting and removal of OE and OE scrap at the site has been partially completed. Soil samples showed levels of benzo(a)pyrene (maximum 22 ppm), and dibenzo(a,h)anthracene (maximum 7.3 ppm) above the human RRSE standard concentrations.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Explosives, Metals, SVOCs, VOCs,

PCBs, Herbicides

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water, Sediment

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

None

FUTURE IRP PHASE:

RI/FS, RD, RA, LTM

PROPOSED PLAN

A RI/FS will be completed. A RD/RA of debris and soil removal may be required.

| Constrained Cost to Complete | | | | | | |
|-------------------------------------|-----------|------|------|-------|--|--|
| | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | |
| RI/FS | | | | 642 | | |
| IRA | | | | | | |
| RD | | | | 80 | | |
| RA | | | | 1156 | | |
| RA(O) | | | | | | |
| LTM | | | | 360 | | |
| | | | | | | |
| Total | 2,238,000 | | | | | |



RVAAP-51

DUMP ALONG PARIS-WINDHAM RD.

SITE DESCRIPTION

This AOC is an area adjacent to Sand Creek that was used as an open dump for miscellaneous materials including transite siding, lab bottles and drums. The site is $400 \times 20 \times 3$ ft deep. The dates of operation for the dump are unknown, but aerial photos show the site in the 1950s.

The surface soil and sediment pathway are considered complete. Three surface soil samples and one sediment sample were collected and analyzed for SVOCs, explosives and metals. Soil samples were taken by USACE in September 2001 to further refine the RRSE. The most significant contaminants were organics including benzo(a)anthracene (3.45 ppm), benzo(a)pyrene (3.38 ppm), benzo(b)fluoranthene (4.65 ppm), chrysene (2.91 ppm) and Indeno(1,2,3-cd)pyrene (2 ppm). The high RRSE rating was confirmed by this sampling event.

A soil and debris removal action was completed in fall 2003.

PROPOSED PLAN

A removal report will be prepared in winter 2003-4.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals, SVOCs

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water,

Sediment

COMPLETED IRP PHASE:

PA/SI, RI/FS, RD

CURRENT IRP PHASE:

RA (funded), LTM

FUTURE IRP PHASE:

LTM

| Constr | Constrained Cost to Complete | | | | | | | | | | | | | |
|--------|------------------------------|------|------|-------|--|--|--|--|--|--|--|--|--|--|
| | _ | | | | | | | | | | | | | |
| | 2004 | 2005 | 2006 | 2007+ | | | | | | | | | | |
| RI/FS | | | | | | | | | | | | | | |
| IRA | | | | | | | | | | | | | | |
| RD | | | | | | | | | | | | | | |
| RA | | | | | | | | | | | | | | |
| RA(O) | | | | | | | | | | | | | | |
| LTM | 40 | 14 | | | | | | | | | | | | |
| | | • | • | • | | | | | | | | | | |
| Total | | 54 | ,000 | | | | | | | | | | | |



Ravenna AAP - Installation Action Plan Site Descriptions - Page 33

RESPONSE COMPLETE SITES

RVAAP-03 **OPEN DEMOLITION AREA #1**

SITE DESCRIPTION

This is a 6 acre AOC that was used for the purpose of thermal treatment of munitions by burning and detonation. The AOC consists of a circular 1 to 1.5 ft berm surrounding a grassy area ~1 to 1.5 acres in size and a pushout area. Operations took place in ~8 foot deep unlined pits. The whole AOC is within the NACA Test Area (RVAAP-38). Contaminants of concern at this AOC include explosive compounds and metals. There is potential for release of contaminants from this unit to the surrounding soils and groundwater. Munitions fragments, including scrap metal, small arms primers, and fuzes, were found outside the bermed area. The AOC was operational from 1941 through 1949 (Jacobs Engineering 1989).

The Phase I RI field work was completed at the site in Oct 1999 and was finalized in 2002. An IRA was started in Nov 2000 and was conducted along with a project funded by OSC to remove UXO from the site. The purpose of the IRA was to remove obvious surface contamination that could pose an immediate risk to human health and the environment. These hot spots are located primarily in an area outside the horseshoe where munitions and scrap were pushed after detonation. The IRA field work was completed in Jul 2001, removing ~83,000 lbs of ordnance explosive waste

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil

COMPLETED IRP PHASE:

PA/SI, RI, IRA

CURRENT IRP PHASE:

RC

Groundwater monitoring at this AOC will be addressed under NACA Test Area (RVAAP-38).

RVAAP-07 **BLDG. 1601 HAZARDOUS WASTE STORAGE**

SITE DESCRIPTION

and UXO.

This site is not eligible for ER,A funds.

This is a RCRA storage facility for solid ash residue and spent activated carbon. It was operated under interim status from 1980 to 1998. No hazardous wastes are currently being stored in the building. The Part B permit application covering the facility was withdrawn during 1994. The building is a 20 by 22 foot concrete igloo. Wastes stored in this building were containerized in 55 gallon DOT drums. There is little potential for contamination resulting from operation of this unit. Closure plans were approved and implemented in 1998.

This site has been officially closed by Ohio EPA.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Metals

MEDIA OF CONCERN:

Soil

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RVAAP-14

LOAD LINE 6 EVAPORATION UNIT

SITE DESCRIPTION

This site is not eligible for ER,A funds

From 1981 through 1987, tenant operations at this load line generated building wash down and wastewater, which was discharged into an 18 x 14 x 4 foot concrete tank. This unit was closed under a NPDES closure in 1989. The closure required removal of all contaminated soils associated with the unit. Soil sampling conducted after removal of soils confirmed clean closure of this unit.

This site is RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

NE

CONTAMINANTS:

Explosives, PCB

MEDIA OF CONCERN:

Soil

COMPLETED IRP PHASE:

PA/SI, RA-RCRA Closure

CURRENT IRP PHASE:

RC - 1989

RVAAP-15

LOAD LINE 6 TREATMENT PLANT

SITE DESCRIPTION

This was an active unit in operation since 1987 by Physics International, which closed in 1993. The unit consists of dual activated carbon units for filtration of pink water generated from load line operations. The wastewater treatment system discharged under an NPDES-permitted discharge to the RVAAP sanitary sewer system. Contaminants of concern at this unit are explosive compounds. There is a low potential for releases from this unit.

This site is RC under the IRP because it's not eligible for IRP funding.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Explosives

MEDIA OF CONCERN:

Soil

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RVAAP-17 DEACTIVATION FURNACE

SITE DESCRIPTION

This site is not eligible for ER,A funds.

This unit is a No. 2 oil-fired horizontal rotary retort furnace used for the deactivation of small munition items. It was operated from 1960 through 1983.

The furnace is currently undergoing closure under a RCRA closure plan. Sampling during closure activities indicates heavy metals contamination to the soils surrounding the furnace area. The closure plan calls for the removal of all contaminated soils associated with the unit. Closure plans have been submitted to Ohio EPA. The buildings were demolished and properly disposed of in October and November 1999.

This site in RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Metals

MEDIA OF CONCERN:

Soil

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RC - 1989

RVAAP-18

LOAD LINE 12 PINK WASTE WATER TREATMENT

SITE DESCRIPTION

This site is not eligible for ER,A funds.

This is an active unit, consisting of dual mode activated carbon filters for the treatment of explosive-contaminated wastewater. This unit was operated from 1982 to 1999. The wastewater treatment discharge was regulated under the NPDES permitted discharge system. Contaminants of concern included explosive compounds. The plant and the associated demil building (904) were closed and demolished under the supervision of Ohio EPA in the fall of 1999. A final closure letter was issued by EPA in May 2000.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Explosives

MEDIA OF CONCERN:

Soil, Groundwater

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

SAND CREEK SEWAGE TREATMENT PLANT

SITE DESCRIPTION

This site is not eligible for ER,A funds.

This is an inactive domestic sewage treatment plant regulated under an NPDES discharge permit. This plant is no longer needed by the installation under modified caretaker status, and was closed in FY 1993 in accordance with EPA requirements. There is a low potential for releases to the soil and groundwater from this unit.

This site in RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

NE

CONTAMINANTS:

Explosives, PCB

MEDIA OF CONCERN:

Soil. Groundwater

COMPLETED IRP PHASE:

PΑ

CURRENT IRP PHASE:

RC - 1989

RVAAP-21

DEPOT SEWAGE TREATMENT PLANT

SITE DESCRIPTION

This site is not eligible for ER,A funds.

This is an inactive domestic sewage treatment plant regulated under an NPDES discharge permit. This plant is no longer needed by the installation under modified caretaker status and was closed in FY 1993 in accordance with EPA requirements. There is a low potential for releases to the soil and groundwater from this unit.

This site in RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

NE

CONTAMINANTS:

Metals

MEDIA OF CONCERN:

Soil, Groundwater

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

GEORGE ROAD SEWAGE TREATMENT PLANT

SITE DESCRIPTION

This site is not eligible for ER,A funds.

This is an inactive domestic sewage treatment plant regulated under an NPDES discharge permit. The plant was closed in FY93 in accordance with EPA requirements. There is a low potential for releases to the soil and groundwater from this unit.

This site in RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

NE

CONTAMINANTS:

Metals

MEDIA OF CONCERN:

Soil

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RC - 1989

RVAAP-23

UNIT TRAINING EQUIPMENT SITE UST

SITE DESCRIPTION

This site is not eligible for ER,A funds.

This unit was a underground storage tank for waste oil used by a RVAAP tenant organization. The PA/SI was completed in 1989. The tank, and any associated contaminated soil, were removed in 1989 by the OARNG. Documentation of the removal will be provided to Ohio EPA for final closure by OHARNG.

This site in RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Waste Oil

MEDIA OF CONCERN:

Soil

COMPLETED IRP PHASE:

PA/SI, RA

CURRENT IRP PHASE:

RVAAP-24 WASTE OIL TANK

SITE DESCRIPTION

This site is not eligible for ER,A funds.

This unit is an above-ground storage tank, without secondary containment, for waste oil from the vehicle maintenance operations of an RVAAP tenant organization located in the Depot Area, Bldg. U4, of RVAAP. The tank was used from 1983 to 1993. The contents were emptied and the tank has remained inactive. Contaminants of concern include petroleum and metals. There is a potential for release of contaminants to the surrounding soils and groundwater from this unit.

This site in RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Waste Oil

MEDIA OF CONCERN:

Soil. Groundwater

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RC - 1989

RVAAP-25 BLDG. 1034 MOTOR POOL AST

SITE DESCRIPTION

This site is not eligible for ER,A funds.

This unit is an inactive above-ground storage tank used to store waste oil from RVAAP vehicle maintenance operations. Use of the tank began in 1974 and was emptied of all contents in FY93 and remains inactive. Contaminants of concern include petroleum and metals. There is a low potential for release of contaminants to the surrounding soils and groundwater from this unit.

This site in RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Waste Oil

MEDIA OF CONCERN:

Soil, Groundwater

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

FUZE BOOSTER AREA SETTLING TANKS

SITE DESCRIPTION

The fuze and booster area covers ~450 acres and includes load lines 5, 6, 7, 8, 9, 10 and 11. These load lines were used for the manufacture of miscellaneous fuzes, boosters, primers, detonators and percussion elements from 1941 through 1971. Within the line areas are 14 concrete underground storage tanks and 1 concrete above ground storage tank which were used as settling basins for explosive-contaminated waste water. The tanks were emptied, cleaned and covered in 1971.

Contaminants of concern from these units are explosives, lead, lead azide, lead styphnate, mercury, and unknown compounds. Shallow monitoring wells were installed in 1981 around the perimeter of the fuze and booster area. Subsequent sampling of the wells did not detect heavy metals in the groundwater. The wells were eventually destroyed by frost heave.

This site is RC, because each LL became its own AOC.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RC - 2000

RVAAP-27 BUILDINGS 854, PCB STORAGE

SITE DESCRIPTION

This unit consists of a 50 x 250 ft. area within a wood framed building used for the storage of PCB contaminated materials. All PCB contaminated material was removed from the building and the interior decontaminated to non-detection limits in the summer of 1998.

Ohio EPA issued a closure letter for this site on September 1, 1999.

STATUS

RRSE RATING:

NE

CONTAMINANTS:

PCBs

MEDIA OF CONCERN:

Soil

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RVAAP-30 LL7 TREATMENT PLANT

SITE DESCRIPTION

This AOC is an inactive dual activated carbon pink waste water treatment unit that was used by Physics International from 1989 through 1992. The discharge from the unit was regulated under the NPDES permit system. Contaminants of concern associated with this unit include explosive compounds.

This site is RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Explosives

MEDIA OF CONCERN:

Soil

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RC - 2000

RVAAP-31 ORE PILE RETENTION POND

SITE DESCRIPTION

This unit consists of a small pond constructed to prevent potentially contaminated surface runoff from strategic manganese and chromium ore piles from entering a receiving stream. The pond was constructed in the mid-1950s. There is a potential for release of contaminants from this unit to the surrounding soils, groundwater and surface water/sediment.

This site is RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Maganese, Chromium

MEDIA OF CONCERN:

Soil, Groundwater, Surface Water

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

1037 BUILDING - LAUNDRY WASTEWATER SUMP

SITE DESCRIPTION

This AOC consists of a concrete sump that was used as a settling tank for RVAAP laundry facilities. This sump was in operation from the early 1940s until 1992. No original file documentation exists for this site.

This site is RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

Medium

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:Soil. Groundwater

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

RC - 2000

RVAAP-37 PESTICIDE BUILDINGS S-4452

SITE DESCRIPTION

This unit consists of a 12.2×6.1 meter (40×20 ft) wooden structure with a crawl space, which housed various pesticides. A 6.1×3.6 meter (20×12 ft) pesticide mixing area was also located in a gravel area outside of the building. This unit was in use from the 1970s until 1993. An empty can with chlorinate residue and a hand sprayer were found in the building crawl space. No originial file documentation exists for this site.

The building and soil were removed from the site and properly disposed of in the fall of 1999 in accordance with Ohio EPA guidance and recommendations. No pesticides were detected in the soil following remediation.

This site is RC because it is not eligible for IRP funding.

STATUS

RRSE RATING:

Low

CONTAMINANTS:

Synthetic organic compounds

MEDIA OF CONCERN:

Soil, groundwater

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:

SITE DESCRIPTION

This building was used to clean and decontaminate explosives and propellants from small, miscellaneous production equipment. Quantities and dates of testing are unknown, but should correspond to the dates of production (intermittent from World War II to Vietnam).

The PA/SI was completed in 1998. The surface soil and sediment pathways are considered complete. The surface water pathway is not considered complete because the ditch no longer has water in it. Two surface soil samples were collected outside of the roll-up door adjacent to the concrete floor and one sediment sample was collected from the drainage ditch outside that drains to Sand Creek. All of the samples were analyzed for metals and explosives. A IRA was completed in FY2000. No industrially related contaminants were found in the soil during the confirmation sampling. Lead was detected in the sediment of Sand Creek at levels slightly above the facility background level.

Ohio EPA has issued a letter stating no further action (under ER,A) is needed at this site provided the elevated lead found in the sediment is addressed during the facility-wide surface water investigation.

STATUS

RRSE RATING:

High

CONTAMINANTS:

Explosives, Metals

MEDIA OF CONCERN:

Soil, Sediment

COMPLETED IRP PHASE:

PA/SI

CURRENT IRP PHASE:



PAST MILESTONES

1990

PA, Installation 38 AOCs

1996

PA/RI Action Plan

Phase I RI High Priority Sites

1998

Phase II RI Winklepeck Burning Grounds Field Work Complete/Draft Report under Review Facility-wide Background Field Work Complete/Draft Report currently under Review RRSE for 13 new sites Field Work Complete/Draft Report Currently Under Review

1999

RI - Phase II Erie Burning Grounds

RI - Phase II NACA Test Area

RI - Phase II Open Demolition Area #1

2000

IRA - LL 12/ Bioremediation Pilot Study Demonstration Complete

RI - Phase II Erie Burning Grounds Draft Report Completed/ Under Review

RI - Phase I NACA Test Area Field Work/Draft Report Completed/Under Review

RI - Phase I Open Demolition Area #1 Field Work/Draft Report Completed/ Under Review

RI - Winklepeck Open Burning Grounds Ecological Risk Assessment Field Work Complete

IRA - Building 5301 Completed/No Further Action Status

Facility-Draft Revision to Wide SAP and HSP completed

2001

RI - Phase I Load Line 11 Field Work Complete

RI - Phase II Load Line 1, 12 Field Work Complete

FS - Winklepeck Field Work Completed

RI - Phase I Load Line 11 Field Work Completed

IRA - Open Demolition Area #1 Fieldwork Completed

RI - Load Lines 2,3,4 Fieldwork (Phase II) Completed

RI - Central Burn Pits Phase I Fieldwork Completed

RI - Upper & Lower Cobb Ponds Phase I Fieldwork Completed

2002

RI- Phase II Open Demolition Area #2 Fieldwork Completed

- Work Plans completed for the IRAs at Paris Windham Road Dump (RVAAP-51) and Sand Creek Disposal Road Landfill (RVAAP-34)
- IRA reports for Open Demolitiona Area #1 (RVAAP-03) and Load Line 11 (RVAAP-44) issued
- Work Plans for Open Demolition Area #2 completed
- Draft Final Report for Winklepeck Burning Grounds Biological Field Truthing project issued.
- Work Plans issued for Facility-wide Human Health and Ecological Risk Assements issued.
- Draft Work Plans for Facility-wide surface water assessment issued

2003

PBC for soil/sediment at Load Lines 1, 2, 3 and 4

RI- Field work for LL 6 & 9 and the Fuze & Booster Quarry Landfill Pond Completed



PROJECTED MILESTONES

2014

All Remedies In Place (RIP)

2015+

Long-term Monitoring Complete

NO FURTHER ACTION SITES

| The following | sites currently require no further action under | the ER,A program. |
|---------------|---|-------------------|
| DVAADAA | ODENI DENIOLITIONI ADEA "A | 0000 |

| RVAAP-03 | OPEN DEMOLITION AREA#1 | 2003 |
|----------|----------------------------------|------|
| RVAAP-26 | FUZE BOOSTER AREA SETTLING TANKS | 2000 |
| RVAAP-27 | BUILDING 854, PCB STORAGE | 1989 |
| RVAAP-47 | BUILDING T-5301 | 2001 |

The following sites are not eligible for ER,A funds and will be addressed under other programs.

RVAAP-07 BLDG 1601 HAZ WASTE STORAGE 1989

| RVAAP-07 | BLDG 1601 HAZ WASTE STORAGE | 1989 |
|----------|-------------------------------------|------|
| RVAAP-14 | LOAD LINE 6 EVAPORATION UNIT | 1989 |
| RVAAP-15 | LOAD LINE 6 TREATMENT PLANT | 2000 |
| RVAAP-17 | DEACTIVATION FURNACE | 1989 |
| RVAAP-18 | LOAD LINE 12 WWT PLANT | 1997 |
| RVAAP-20 | SAND CREEK STP | 1989 |
| RVAAP-21 | DEPOT STP | 1989 |
| RVAAP-22 | GEORGE RD STP | 1989 |
| RVAAP-23 | UNIT TRAINING EQUIPMENT SITE UST | 1989 |
| RVAAP-24 | WASTE OIL TANK | 1989 |
| RVAAP-25 | BUILDING 1034 MOTOR POOLAST | 1989 |
| RVAAP-30 | LL7 TREATMENT PLANT | 2000 |
| RVAAP-31 | ORE PILE RETENTION POND | 2000 |
| RVAAP-35 | 1037 BLDG - LAUNDRY WASTEWATER SUMP | 2000 |
| RVAAP-37 | PESTICIDE BUILDING S-4452 | 1996 |
| | | |

Ravenna Army Ammo Plant IAP Schedule

(based on current funding)

| DSERTS # | SITE NAME | PHASE | FY03 | FY04 | FY05 | FY06 | FY07 | FY08 | FY09+ |
|--|---|---|------|------|------|------|------|------|-------|
| RVAAP-01 | Ramsdell Quarry Landfill (H) | RI/FS | | | | | | | |
| | Trainiscen Quarry Earlaini (11) | LTM | | | | | | | |
| RVAAP-02 | Erie Burning Grounds (H) | RI/FS | | | | | | | |
| 107771 02 | Elic Barriing Grounds (11) | LTM | | | | | | | |
| R\/A | Demolition Area #2 (H) | RI/FS | | | | | | | |
| | Demonitori Area #2 (11) | RD | | | | | | | |
| I | | RA | | | | | | | |
| I | | LTM | | | | | | | |
| D) / A A D OF | Windshon and Demain as Conservation | | | | | | | | |
| RVAAP-05 | Winklepeck Burning Grounds | RI/FS | | | | | | | |
| ı | (H) | RD | | | | | | | |
| ı | | RA | | | | | | | |
| D) (4 4 D 6 6 | 1 11 4 (11) | LTM | | | | | | | |
| RVAAP-08 | Load Line 1 (H) | RI/FS | | | | | | | |
| | | RD | | | | | | | |
| İ | | RA | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-12 | Load Line 12 (H) | RI/FS | | | | | | | |
| | | RD | | | | | | | |
| | | RA | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-16 | Fuze and Booster Quarry | RI/FS | | | | | | | |
| ı | Landfill/ Pond (H) | RD | | | | | | | |
| ı | | RA | | | | | | | |
| | | LTM | | | | | | | |
| | Sand Creek Disposal Road | RI/FS | | | | | | | |
| RVAAP-44 | Load Line 11 (H) | RI/FS | | | | | | | |
| <u> </u> | ` , | LTM | | | | | | | |
| RVAAP-46 | Bldg F-15 & F-16 (H) | RI/FS | | | | | | | |
| I | | RD | | | | | | | |
| I | | RA | | | | | | | |
| RVAAP-49 | Central Burn Pits (H) | RI/FS | | | | | | | |
| İ | , , | RD | | | | | | | |
| ı | | RA | | | | | | | |
| ı | | LTM | | | | | | | |
| RVAAP-51 | Dump Along Paris Windham | LTM | | | | | | | |
| | | | | | | | | | |
| RVAAP-11 | Load Line 4 (M) | RI/FS | | | | | | | |
| | | RD | | | | | | | |
| | | 1 1 | | | | | | | |
| | | RA | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-29 | Upper & Lower Cobbs Ponds | LTM RI/FS | | | | | | | |
| | (M) | LTM RI/FS LTM | | | | | | | |
| RVAAP-32 | (M) 40 MM Firing Range (M) | LTM RI/FS LTM RI/FS | | | | | | | |
| RVAAP-32 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster | LTM RI/FS LTM RI/FS RI/FS | | | | | | | |
| RVAAP-32 | (M) 40 MM Firing Range (M) | LTM RI/FS LTM RI/FS RI/FS RD | | | | | | | |
| RVAAP-32 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster | LTM RI/FS LTM RI/FS RI/FS RD RA | | | | | | | |
| RVAAP-32 RVAAP-33 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) | RI/FS LTM RI/FS RI/FS RD RA LTM | | | | | | | |
| RVAAP-32 RVAAP-33 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster | RI/FS LTM RI/FS RI/FS RD RA LTM RD | | | | | | | |
| RVAAP-32 RVAAP-33 RVAAP-36 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) Pistol Range (M) | RI/FS LTM RI/FS RI/FS RD RA LTM RD RA | | | | | | | |
| RVAAP-32 RVAAP-33 RVAAP-36 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) | RI/FS LTM RI/FS RI/FS RI/FS RD RA LTM RD RA RI/FS | | | | | | | |
| RVAAP-32 RVAAP-33 RVAAP-36 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) Pistol Range (M) | RI/FS LTM RI/FS RI/FS RD RA LTM RD RA RI/FS RD RA RD RA RI/FS RD | | | | | | | |
| RVAAP-32 RVAAP-33 RVAAP-36 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) Pistol Range (M) | RI/FS LTM RI/FS RI/FS RI/FS RD RA LTM RD RA RI/FS | | | | | | | |
| RVAAP-32 RVAAP-33 RVAAP-36 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) Pistol Range (M) | RI/FS LTM RI/FS RI/FS RD RA LTM RD RA RI/FS RD RA RD RA RI/FS RD | | | | | | | |
| RVAAP-32 RVAAP-33 RVAAP-36 RVAAP-38 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) Pistol Range (M) | RI/FS LTM RI/FS RI/FS RD RA LTM RD RA RI/FS RD RA RI/FS RA RI/FS RD | | | | | | | |
| RVAAP-32 RVAAP-33 RVAAP-36 RVAAP-38 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) Pistol Range (M) NACA Test Area (M) Load Line 5 Fuze and Booster | RI/FS RI/FS RI/FS RD RA LTM RI/FS RD RA LTM RD RA RI/FS RD RA RI/FS RD RA RI/FS | | | | | | | |
| RVAAP-32 RVAAP-33 RVAAP-36 RVAAP-38 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) Pistol Range (M) NACA Test Area (M) | RI/FS RI/FS RI/FS RD RA LTM RI/FS RD RA LTM RD RA RI/FS RD RA RI/FS RD RA LTM RA RI/FS RD RA LTM RI/FS RD | | | | | | | |
| RVAAP-32 RVAAP-33 RVAAP-36 RVAAP-38 | (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) Pistol Range (M) NACA Test Area (M) Load Line 5 Fuze and Booster | RI/FS RI/FS RI/FS RD RA LTM RI/FS RD RA LTM RD RA RI/FS RD RA RI/FS RD RA RI/FS | | | | | | | |

| DSERTS# | SITE NAME | PHASE | FY03 | FY04 | FY05 | FY06 | FY07 | FY08 | FY09+ |
|-----------|-------------------------------|-------|------|------|------|------|------|------|-------|
| | (M) | RD | | | | | | | |
| | <u>`</u> | RA | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-42 | Load Line 9 Fuze and Booster | RI/FS | | | | | | | |
| | (M) | RD | | | | | | | |
| | | RA | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-43 | Load Line 10 Percussion | RI/FS | | | | | | | |
| | Element (M) | RD | | | | | | | |
| | | RA | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-48 | Anchor Test Area (M) | RI/FS | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-50 | Atlas Scrap Yard (M) | RI/FS | | | | | | | |
| | | RD | | | | | | | |
| | | RA | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-06 | C Block Quarry (L) | RI/FS | | | | | | | |
| 107011 00 | Blook Quarry (E) | RD | | | | | | | |
| | | RA | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-13 | Bldg. 1200 (L) | RI/FS | | | | | | | |
| | J.ag. 1200 (2) | RD | | | | | | | |
| | | RA | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-19 | Landfill North of Winklepeck | RI/FS | | | | | | | |
| | Burning Ground (L) | RD | | | | | | | |
| | - ag | RA© | | | | | | | |
| | | RA(O) | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-28 | Mustard Agent Burial Site (L) | RI/FS | | | | | | | |
| RVAAP-40 | Load Line 7 Fuze and Booster | RI/FS | | | | | | | |
| | (L) | RD | | | | | | | |
| | ` ' | RA | | | | | | | |
| | | LTM | | | | | | | |
| RVAAP-45 | Wet Storage Area (L) | RI/FS | | | | | | | |
| | | IRA | | | | | Ì | | |

REM/IRA/RA ASSESSMENT

Past REM/IRA/RA

- RVAAP-03, Open Demo Area #1
- RVAAP-12, Load Line 12 IRA- Composting
- RVAAP-34 IRA- Waste removal 2002
- RVAAP-47, Building T-5301 IRA
- RVAAP-51 IRA- Waste removal 2002

Current REM/IRA/RA

- None

Future REM/IRA/RA

RVAAP-04, 05, 06, 08, 09 (PBC), 10 (PBC), 11 (PBC), 12, 13, 16, 19, 33, 36, 38, 39, 40, 41, 42, 43, 45, 46, 49, 50

PRIOR YEAR FUNDING

| FY 1994 | Scoping | \$9,371.88 | \$9,371.88 |
|----------|----------------------------------|----------------|-----------------------|
| FY 1995 | Group A Site/RI | \$225,207.33 | |
| 1 1 1000 | Group A | \$1,007,114.03 | \$1,232,321.36 |
| | Cloup | ψ1,007,111.00 | Ψ1,202,021.00 |
| FY 1996 | Phase I RFI | \$15,000 | |
| | Winklepeck Burning Grounds | \$21,460.64 | |
| | Demo Area 2 | \$2,259.78 | |
| | Load Line #1 Dil/ Set Ponds | \$23,722.57 | |
| | Load Line #12 Dil/Set | \$19,620.97 | |
| | Landfill/ Winklepeck | \$2,101.08 | |
| | Load Line #12 Pink Waste | \$2,279.6 | |
| | Load Line #3 Dil/Set | \$20,502.48 | |
| | Load Line #4 Dil/Set | \$2,287.58 | |
| | Upper & Lower Cobb Pond | \$2,279.6 | |
| | Load Line #2 Dil/Set | \$21,994.65 | |
| | RI/FS Group A Sites | \$200,319.16 | \$333,828.11 |
| | Mil o Group A Gites | Ψ200,313.10 | ψ555,020.11 |
| FY 1997 | RAB Support | \$21,590.43 | |
| 1 1 1007 | Mustard Agent Burial Site | \$23,664.74 | |
| | Winklepeck Burning Ground | \$1,230,226.72 | |
| | Firestone Test Fac., SI | \$50,000 | \$1,325,481.89 |
| | 1 110010110 10011 401, 01 | 400,000 | ψ.,σ2σ, .σσσ |
| FY 1998 | RAB Support | \$23,320.96 | |
| | Burning Grounds | \$10,000 | |
| | GIS Database Dev P.O. | \$28,991.12 | \$62,312.08 |
| = 1,1000 | | * | |
| FY 1999 | Winklepeck Burning Ground | \$75,000 | |
| | NACA Test RI/FS | \$12,000 | |
| | Load Line #1 RI/FS | \$65,000 | |
| | Erie Burning Ground RI/FS | \$761,389 | |
| | Demo Area #1 | \$42,931 | |
| | NACA Test Area | \$43,069 | |
| | RAB Support | \$20,000 | |
| | Winklepeck Data Project Order | \$20,000 | |
| | Winklepeck Wells Project Order | \$20,000 | |
| | NACA Test Area | \$386,788 | . |
| | Load Line #1 Phase II RI | \$25,000 | \$1,471,177 |
| FY 2000 | Erie Burning Grounds RI | \$39,200 | |
| 2000 | Open Demolition Area #1 IRA | \$401,100 | |
| | Open Demolition Area #1 RI | \$350,500 | |
| | Open Demolition Area #2 RI | \$45,500 | |
| | Winklepeck Burning Grounds RI/FS | \$1,432,900 | |
| | Load Line I RI | \$230,000 | |
| | Load Line 12 RI | \$1,239,800 | |
| | Load Line 12 IRA | \$408,700 | |
| | NACA Test Area RI/FS | \$138,800 | |
| | Load Line 11 RI | \$525,000 | |
| | Load Line 11 RI | \$975,000 | |
| | 2000 2010 1110 | 40.0,000 | Rayenna AAP - Install |

PRIOR YEAR FUNDING

| | Building T-5301 | \$215,000 | \$6,001,500 |
|------------|--|--|--------------|
| FY 2001 | Erie Burning Grounds RI/FS Open Demolition Area #1 RI/FS Open Demolition Area #2 RI/FS Winklepeck Burning Grounds RI/FS Load Line 1 RI/FS Load Line 2 RI/FS Load Line 3 RI/FS Load Line 4 RI/FS Load Line 12 RI/FS Upper & Lower Cobb Ponds RI/FS Sand Creek Disposal Road Landfill NACA Test Area Load Line II RI/FS Central Burn Pits RI/FS Dump Along Paris-Windham Road RD | \$25,000 \$30,000 \$689,300 \$157,200 \$33,000 \$1,208,300 \$642,300 \$681,000 \$21,000 \$496,500 \$20,000 \$20,000 \$186,800 \$630,000 \$10,000 | \$4,850,400 |
| FY 2002 | Open Demolition Area #1 Open Demolition Area #2 Winklepeck Burning Grounds C Block Quarry Load Line 1 Load Line 2 Load Line 3 Load Line 4 Load Line 12 Upper & Lower Cobb Ponds Load Line 6 Sand Creek Disposal Road Landfill NACA Test Area Load Line 9 Central Burn Pits Dump Along Paris-Windham Road | \$17,300 \$71,100 \$403,900 \$5,000 \$39,100 \$42,600 \$204,900 \$101,700 \$41,300 \$21,900 \$804,800 \$472,800 \$18,300 \$794,200 \$23,800 \$188,800 | \$3,251,600 |
| FY03 | including \$9,836,280 for PBC | | \$13,259,430 |
| TOTAL PRIC | R YEARS FUNDING | \$23,386,992.32 | |
| | | | |

ESTIMATED TOTAL FUTURE REQUIREMENTS (FY04+) \$36,718,000

| DSERTS | SITE TITLE | | | | | | | | | PHASE | SITE | |
|---------------|--------------------|----------|-----------|-------|-------|------|------|------|-------|-----------|-------|--|
| # | (RRSE) | PHASE | FY04 | FY05 | FY06 | FY07 | FY08 | FY09 | FY10+ | | TOTAL | DESCRIPTION OF WORK |
| RVAAP- | Ramsdell Quarry | RI/FS | 156 | 420 | | | | | | 576 | | install 6 wells, 4 sampling events,15 soil, detailed data analysis, |
| | Landfill (H) | | | | | | | | | | | Risk Assessment |
| | | LTM | | | 434 | 30 | 30 | 30 | 90 | 614 | | 12 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 1,190 | closure report (40K/yr is combination of S&R and QA/QC) |
| RVAAP- | Erie Burning | RI/FS | 16 | 122 | | | | | | 138 | | additional sampling 15 soil, 12SW/sediment, 8 wells, RI report, |
| 02 | Grounds (H) | | | | | | | | | | | HH & Eco Risk Characterization, UXO support needed |
| | | | | | | | | | | | | |
| | | LTM | | 35 | 30 | 30 | | | | 95 | 233 | ~8 wells, semi-annual, Final Report |
| | | RI/FS | 145 | 100 | | | | | | 245 | | Finalize RI report |
| 04 | | RD | | 18 | | | | | | 18 | | design of RA |
| | | RA | | | 1,025 | 40 | | | | 1,065 | | soil removal 500cy Haz, 1,600cy removal for bank stabilization |
| | | | | | | | | | | | | ~75ft, closure report |
| | | LTM | | | | 699 | 40 | 40 | 880 | 1,659 | | LTM-16 wells, 3 SWs, 6 times/year for 2 yrs, then 8 wells, semi- |
| | | | | | | | | | | | 2,987 | annual for 8 years, Closure report |
| | | RI/FS | 40 | | | | | | | 40 | | Ongoing FS, finalize reports, S&R |
| 05 | Burning Grounds | | 69 | | | | | | | 69 | | design of RA |
| | (H) | RA | | 1,000 | | | | | | 1,000 | | Assuming soil removal to 4 ft bgs at ~8 pads (~12,000cy), |
| | | | | | | 4.0 | 4.0 | 10 | 100 | 1 000 | | Screen for explosives, compost & stabil (UXO avoidance) |
| | | LTM | | | 760 | 40 | 40 | 40 | 120 | 1,000 | 0.400 | ~17 wells, quarterly for 2 yrs, semi for 1 yrs, annual for 2 yrs, |
| D) / A A D | 4 / | חוירס | 50 | | | | | | | 50 | 2,109 | closure reports |
| | ` ' | RI/FS | 50 | 10 | | | | | | 50 10 | | finalize FS |
| 08 | | RD RA | | 30 | 40 | 20 | | | | 90 | | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs |
| | | KA | | 30 | 40 | 20 | | | | 90 | | shown are in-house for COE |
| | | LTM | | | | | 168 | 20 | 80 | 268 | | 13 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | LIIVI | | | | | 100 | 20 | 80 | 200 | 418 | closure report |
| RVAAP- | Load Line 2 (H) | | | | | | | | | | 410 | PBC |
| | Load Line 3 (H) | | | | | | | | | | | PBC |
| | Load Line 12 (H) | | | | | | | | | | | PBC |
| 12 | 2000 2.110 12 (11) | | | | | | | | | | | . 50 |
| | Fuze and | RI/FS | 487 | 540 | 120 | | | | | 1,147 | | RI/FS including 12 wells, sediment, surface, and soil samples |
| | Booster Quarry | | | | | | | | | ., | | (UXO complication), Eco data gaps 60K, Facility Wide GW set |
| | Landfill/ Pond | | | | | | | | | | | up in FY05 500K |
| | (H) | RD | | | | 15 | | | | 15 | | design of RA |
| | | RA | | | | | 400 | 166 | | 566 | | Sediment (1,600cy) & debris removal from ponds, lagoon |
| | | LTM | | | | | | 335 | 100 | 435 | | 12 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 2,163 | closure report |
| | | | | | | | | | | | | |

| DSERTS | SITE TITLE | | | | | | | | | PHASE | SITE | |
|--|--|---|-----------------|------------------|------|------|------|-----------|-------|---|-----------------------|---|
| # | (RRSE) | PHASE | FY04 | FY05 | FY06 | FY07 | FY08 | FY09 | FY10+ | TOTAL | TOTAL | DESCRIPTION OF WORK |
| RVAAP- | Sand Creek | RI/FS | 60 | | | | | | | 60 | | finalize IRA report, site closure including assessment of residual |
| 34 | Disposal Road | | | | | | | | | | | asbestos |
| | Landfill (H) | | | | | | | | | | 60 | |
| RVAAP- | Load Line 11 (H) | RI/FS | 40 | | | | | | | 40 | | finalize IRA and RI report |
| 44 | | LTM | | 449 | 20 | 20 | 20 | 20 | 20 | 549 | | 10 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 589 | closure report |
| | • | RI/FS | 192 | 20 | 147 | | | | | 359 | | sampling 2 areas |
| 46 | ` ' | RD | | | | 34 | | | | 34 | | design of RA |
| | | RA | | | | | 420 | 54 | | 474 | | sediment removal 200cy for explosives & metals, closure docs |
| | | | | | | | | | | | 867 | |
| | Central Burn Pits | | 284 | 120 | | | | | | 404 | | finalize RI, FS, Eco data gaps 60K |
| 49 | \ / | RD | | 16 | 001 | | | | | 16 | | design of RA |
| | | RA | | | 804 | | | 0.0 | | 804 | | metals fixation 1,000cy, removal 500cy |
| | | LTM | | | | 552 | 30 | 30 | 90 | 702 | 4 000 | 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| D) (A A D | D Al | 1 Th 4 | 40 | 4.4 | | | | | | E 4 | 1,926 | closure report |
| RVAAP- | 1 5 | LTM | 40 | 14 | | | | | | 54 | | 4 wells, quarterly for 2 yrs, semi-annual for 1 yr, annual for 2 yrs, |
| 51 | Paris Windham | | | | | | | | | | 54 | closure reports |
| | Rd. (H) | | | | | | | | | | 54 | |
| | | | | | | | | | | | | |
| RVAAP- | Load Line 4 (M) | RI/FS | 50 | | | | | | | 50 | | finalize FS |
| RVAAP- 11 | , , | RD | 50 | 10 | | | | | | 10 | | design of RA |
| | , , | | 50 | 10 | 40 | 20 | | | | | | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs |
| | , , , | RD RA | 50 | | 40 | 20 | | | | 10 90 | | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE |
| | , , , | RD | 50 | | 40 | 20 | 168 | 20 | 80 | 10 | | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| 11 | | RD RA LTM | | 30 | 40 | 20 | 168 | 20 | 80 | 10 90 268 | 418 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report |
| 11 RVAAP- | Upper & Lower | RD RA | 50 49 | | 40 | 20 | 168 | 20 | 80 | 10 90 | 418 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of |
| 11 | Upper & Lower Cobbs Ponds | RD RA LTM RI/FS | | 204 | | | | | | 10 90 268 253 | 418 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of facility-wide surface water study. |
| 11 RVAAP- | Upper & Lower Cobbs Ponds | RD RA LTM | | 30 | 40 | 20 | 168 | 20 | 80 | 10 90 268 | | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of facility-wide surface water study. 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| RVAAP- 29 | Upper & Lower Cobbs Ponds (M) | RD RA LTM RI/FS LTM | 49 | 204 | | | 30 | 30 | | 10 90 268 253 759 | 1,012 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of facility-wide surface water study. 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report |
| RVAAP- 29 | Upper & Lower Cobbs Ponds (M) | RD RA LTM RI/FS | | 204 | | | | | | 10 90 268 253 | 1,012 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of facility-wide surface water study. 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| RVAAP- 29 RVAAP- 32 | Upper & Lower Cobbs Ponds (M) 40 MM Firing Range (M) | RD RA LTM RI/FS LTM | 49 | 30 204 609 | 30 | 30 | 30 | 30 | | 10 90 268 253 759 334 | 1,012 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of facility-wide surface water study. 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report sampling with UXO precautions |
| RVAAP- 29 RVAAP- 32 RVAAP- | Upper & Lower Cobbs Ponds (M) 40 MM Firing Range (M) Load Line 6 | RD RA LTM RI/FS LTM RI/FS RI/FS | 49 | 204 | | | 30 | 30 | | 10 90 268 253 759 334 316 | 1,012 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of facility-wide surface water study. 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report sampling with UXO precautions RI/FS including GW, Eco data gaps 60K |
| RVAAP- 29 RVAAP- 32 | Upper & Lower Cobbs Ponds (M) 40 MM Firing Range (M) Load Line 6 Fuze and | RD RA LTM RI/FS LTM RI/FS RI/FS RD | 49 | 30 204 609 | 30 | 30 | 30 | 30 | | 10 90 268 253 759 334 316 17 | 1,012 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of facility-wide surface water study. 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report sampling with UXO precautions RI/FS including GW, Eco data gaps 60K design of RA |
| RVAAP- 29 RVAAP- 32 RVAAP- | Upper & Lower Cobbs Ponds (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) | RD RA LTM RI/FS LTM RI/FS RI/FS RD RA | 49 | 30 204 609 | 30 | 30 | 30 | 30 30 747 | 30 | 10 90 268 253 759 334 316 17 747 | 1,012 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of facility-wide surface water study. 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report sampling with UXO precautions RI/FS including GW, Eco data gaps 60K design of RA soil removal 2,000cy |
| RVAAP- 29 RVAAP- 32 RVAAP- | Upper & Lower Cobbs Ponds (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) | RD RA LTM RI/FS LTM RI/FS RI/FS RD | 49 | 30 204 609 | 30 | 30 | 30 | 30 | | 10 90 268 253 759 334 316 17 | 1,012 334 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of facility-wide surface water study. 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report sampling with UXO precautions RI/FS including GW, Eco data gaps 60K design of RA soil removal 2,000cy 10 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| RVAAP- 29 RVAAP- 32 RVAAP- 33 | Upper & Lower Cobbs Ponds (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) | RD RA LTM RI/FS LTM RI/FS RI/FS RD RA LTM | 49 20 136 | 30 204 609 | 30 | 30 | 30 | 30 30 747 | 30 | 10 90 268 253 759 334 316 17 747 769 | 1,012 334 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of facility-wide surface water study. 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report sampling with UXO precautions RI/FS including GW, Eco data gaps 60K design of RA soil removal 2,000cy 10 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report |
| RVAAP- 29 RVAAP- 32 RVAAP- | Upper & Lower Cobbs Ponds (M) 40 MM Firing Range (M) Load Line 6 Fuze and Booster (M) | RD RA LTM RI/FS LTM RI/FS RI/FS RD RA LTM | 49 | 30 204 609 | 30 | 30 | 30 | 30 30 747 | 30 | 10 90 268 253 759 334 316 17 747 | 1,012 334 1,849 | design of RA RA funded in FY03 under FPR= Soil removal ~2,000cy, costs shown are in-house for COE 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report Finalize RI. HH & Eco risk Eco sampling to be done as part of facility-wide surface water study. 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, closure report sampling with UXO precautions RI/FS including GW, Eco data gaps 60K design of RA soil removal 2,000cy 10 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |

| DSERTS | SITE TITLE | | | | | | | | • | PHASE | SITE | |
|---------------|-------------------|-------------|------|------|-------|-------|-------|-------|---------|-------|--------|---|
| # | (RRSE) | PHASE | FY04 | FY05 | FY06 | FY07 | FY08 | EVNO | FY10+ | TOTAL | | DESCRIPTION OF WORK |
| | NACA Test Area | | 145 | 332 | 1 100 | 1 107 | 1 100 | 1 103 | 1 1 10+ | 477 | IOIAL | RI/FS including 12 wells, Risk HH & eco, Eco data gaps 60K |
| | (M) | 11/1 5 | 143 | 332 | | | | | | 7// | | Triff o including 12 wells, trisk till & eco, Eco data gaps ook |
| 30 | ` ' | RD | | 24 | | | | | | 24 | | design of RA |
| | | RA | | 24 | 237 | | | | | 237 | | soil bio remediation 2 acres |
| | | LTM | | | 414 | 30 | 30 | 30 | 60 | 564 | 1 302 | 12 wells, starting at quarterly, closure report |
| RVAAP- | Load Line 5 | RI/FS | | | 414 | 997 | 40 | 120 | 00 | 1,157 | 1,302 | RI/FS including GW, Eco data gaps 60K |
| 39 | | RD | | | | 331 | 40 | 120 | 8 | 8 | | design of RA |
| | | RA | | | | | | | 258 | 258 | | soil/sump removal 20cy |
| | | LTM | | | | | | | 369 | 369 | | 6 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | L I IVI | | | | | | | 309 | 309 | 1 702 | closure report |
| RVAAP- | Load Line 8 | RI/FS | | | | 997 | 40 | 120 | | 1,157 | 1,732 | RI/FS including GW, Eco data gaps 60K |
| | | RD | | | | 331 | 40 | 120 | 8 | 8 | | design of RA |
| 7 | | RA | | | | | | | 258 | 258 | | soil/sump removal 20cy |
| | | LTM | | | | | | | 369 | 369 | | 6 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | 303 | 303 | 1,792 | |
| RVAAP- | Load Line 9 | RI/FS | 118 | 83 | | | | | | 201 | 1,7 52 | RI/FS including GW, Eco data gaps 60K |
| | | RD | 110 | - 00 | 8 | | | | | 8 | | design of RA |
| | | RA | | | 0 | 258 | | | | 258 | | soil/sump removal 20cy |
| | | LTM | | | | 200 | 197 | 20 | 80 | 297 | | 6 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | _ 1 1 1 1 1 | | | | | 107 | 20 | 00 | 201 | 764 | closure report |
| RVAAP- | Load Line 10 | RI/FS | | | | 1,069 | 40 | 120 | | 1,229 | 701 | RI/FS including GW, Eco data gaps 60K |
| | | RD | | | | ., | | 0 | 8 | 8 | | design of RA |
| | | RA | | | | | | | 258 | 258 | | soil/sump removal 20cy |
| | | LTM | | | | | | | 297 | 297 | | 6 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | 20. | 20. | 1.792 | closure report |
| RVAAP- | Anchor Test | RI/FS | | | | | | 200 | 84 | 284 | .,. == | Phase II RI |
| | | LTM | | | | | | | 1,137 | 1,137 | 1,421 | 4 wells, semi-annual |
| | Atlas Scrap Yard | | | | | | | 492 | 150 | 642 | ., | UXO support - 100 soil locations, ~6-8 wells, ~8 sediment, 2 |
| 50 | (M) | | | | | | | | | • .= | | surface water, Risk, eco, Eco data gaps 60K |
| | ` ' | RD | | | | | | | 80 | 80 | | design of RA |
| | | RA | | | | | | | 1,156 | 1,156 | | debis and soil removal |
| | | LTM | | | | | | | 360 | 360 | | 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 2,238 | closure report |
| | C Diagle Occasion | DI/EQ | | | | | | | 005 | 005 | | · |
| | • | RI/FS | | | | | | | 965 | 965 | | RI/FS, DD |
| 06 | ` ' | RD | | | | | | | 33 | 33 | | design of RA |
| | | RA | | | | | | | 1,893 | 1,893 | | Soil removal ~5,000cy |
| | | LTM | | | | | | | 454 | 454 | 2 245 | 4 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 3,345 | closure report |

| DSERTS | SITE TITLE | | | | | | | | | PHASE | SITE | |
|---------------|-------------------|--------------|-------|--------|----------|----------|-------|-------|--------|--------|--------------|---|
| # | (RRSE) | PHASE | FY04 | FY05 | FY06 | FY07 | FY08 | FY09 | FY10+ | TOTAL | TOTAL | DESCRIPTION OF WORK |
| RVAAP- | Bldg. 1200 (L) | RI/FS | | | | | | | 686 | 686 | | complete a RI/FS |
| 13 | | RD | | | | | | | 5 | 5 | | design of RA |
| | | RA | | | | | | | 213 | 213 | | 200cy soil removal |
| | | LTM | | | | | | | 400 | 400 | | 4 wells, quarterly for 2 yrs, semi-annual for 1 yr, annual for 2 yrs, |
| | | | | | | | | | | | 1,304 | closure reports |
| RVAAP- | Landfill North of | RI/FS | | | | | | | 611 | 611 | | Additional RI/FS including 4 wells |
| 19 | Winklepeck | RD | | | | | | | 41 | 41 | | design of RA |
| | Burning Ground | RA | | | | | | | 988 | 988 | | Limit soil cover (2 ft) on ~2.5 acres |
| | (L) | RA(O) | | | | | | | 66 | 66 | | cap maintenance |
| | | LTM | | | | | | | 210 | 210 | | 4 wells, quarterly for 2 yrs, semi-annual for 1 yr, annual for 2 yrs, |
| | | | | | | | | | | | 1,916 | closure reports |
| RVAAP- | Mustard Agent | RI/FS | 162 | | | | | | | 162 | | install 4 wells |
| | Burial Site (L) | | | | | | | | | | 162 | |
| RVAAP- | | RI/FS | | | | | | | 1,157 | 1,157 | | RI/FS including GW, Eco data gaps 60K |
| 40 | | RD | | | | | | | 8 | 8 | | design of RA |
| | Booster (L) | RA | | | | | | | 258 | 258 | | soil/sump removal 20cy |
| | | LTM | | | | | | | 369 | 369 | | 6 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 1,792 | closure report |
| RVAAP- | Wet Storage | RI/FS | | | | | | | 359 | 359 | | complete RI, site closure |
| | | RA | | | | | | | 120 | 120 | 479 | soil removal ~50cy |
| | ALS IN THOUSA | | | | | | 1,994 | 3,233 | 15,466 | 36,718 | 36,718 | |
| Estimates | have been based | d on the F | RACER | systen | n unless | s noted. | | | | | 36,718 | |

| DSERTS | | | | | | | | | | PHASE | SITE | |
|---------------|-----------------------|---------|------|------|-------|------|------|------|-------|-------|-------|--|
| # | SITE TITLE (RRSE) | PHASE | FY04 | FY05 | FY06 | FY07 | FY08 | FY09 | FY10+ | TOTAL | | DESCRIPTION OF WORK |
| RVAAP- | Ramsdell Quarry | RI/FS | 156 | | 420 | | | | | 576 | | install 6 wells, 4 sampling events,15 soil, detailed data |
| 01 | Landfill (H) | | | | | | | | | | | analysis, Risk Assessment |
| | , , | LTM | | | | 434 | 30 | 30 | 120 | 614 | | 12 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | | closure report (40K/yr is combination of S&R and QA/QC) |
| | | | | | | | | | | | 1,190 | |
| RVAAP- | Erie Burning Grounds | RI/FS | 16 | 122 | | | | | | 138 | | additional sampling 15 soil, 12SW/sediment, 8 wells, RI |
| 02 | (H) | | | | | | | | | | | report, HH & Eco Risk Characterization, UXO support |
| | | | | | | | | | | | | needed |
| | | LTM | | 35 | 30 | 30 | | | | 95 | 233 | ~8 wells, semi-annual, Final Report |
| | Demolition Area #2 | RI/FS | 145 | 100 | | | | | | 245 | | Finalize RI report |
| 04 | (H) | RD | | 18 | | | | | | 18 | | design of RA |
| | | RA | | | 1,025 | 40 | | | | 1,065 | | soil removal 500cy Haz, 1,600cy removal for bank |
| | | | | | | | | | | | | stabilization ~75ft, closure report |
| | | LTM | | | | 699 | 40 | 40 | 880 | 1,659 | | LTM-16 wells, 3 SWs, 6 times/year for 2 yrs, then 8 wells, |
| | | | | | | | | | | | 2,987 | semi-annual for 8 years, Closure report |
| | | RI/FS | 40 | | | | | | | 40 | | Ongoing FS, finalize reports, S&R |
| 05 | Grounds (H) | RD | 69 | | | | | | | 69 | | design of RA |
| | | RA | | 600 | 400 | | | | | 1,000 | | Assuming soil removal to 4 ft bgs at ~8 pads (~12,000cy), |
| | | | | | | | | | | | | Screen for explosives, compost & stabil (UXO avoidance) |
| | | LTM | | | 760 | 40 | 40 | 40 | 120 | 1,000 | | ~17 wells, quarterly for 2 yrs, semi for 1 yrs, annual for 2 |
| | | L I IVI | | | 760 | 40 | 40 | 40 | 120 | 1,000 | 2,109 | |
| RVAAP- | Load Line 1 (H) | RI/FS | 50 | | | | | | | 50 | 2,109 | finalize FS |
| 08 | Load Line 1 (11) | RD | 50 | 10 | | | | | | 10 | | design of RA |
| 00 | | RA | | 30 | 40 | 20 | | | | 90 | | RA funded in FY03 under FPR= Soil removal ~2,000cy, |
| | | 10/1 | | 50 | 40 | 20 | | | | 30 | | costs shown are in-house for COE |
| | | LTM | | | | | 168 | 20 | 80 | 268 | | 13 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | 100 | 20 | | 200 | 418 | closure report |
| RVAAP- | Load Line 2 (H) | | | | | | | | | | | PBC |
| | Load Line 3 (H) | | | | | | | | | | | PBC |
| | Load Line 12 (H) | | | | | | | | | | | PBC |
| 12 | () | | | | | | | | | | | |
| RVAAP- | Fuze and Booster | RI/FS | 487 | 540 | 120 | | | | | 1,147 | | RI/FS including 12 wells, sediment, surface, and soil |
| 16 | Quarry Landfill/ Pond | | | | | | | | | | | samples (UXO complication), Eco data gaps 60K, Facility |
| | (H) | | | | | | | | | | | Wide GW set up in FY05 500K |
| | | RD | | | | 15 | | | | 15 | | design of RA |
| | | RA | | | | | 400 | 166 | | 566 | | Sediment (1,600cy) & debris removal from ponds, lagoon |
| | | | | | | | | | | | | |
| | | LTM | | | | | | 335 | 100 | 435 | | 12 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 2 162 | closure report |

| DSERTS | | | | | | | | | | PHASE | SITE | |
|---------------|-----------------------|-------|------|-------|-------|-------|-------|-------|-------|-------|-------|---|
| # | SITE TITLE (RRSE) | PHASE | FY04 | FY05 | FY06 | FY07 | FY08 | FY09 | FY10+ | TOTAL | | DESCRIPTION OF WORK |
| RVAAP- | | RI/FS | 60 | 1 100 | 1 100 | 1 101 | 1 100 | 1 100 | | 60 | TOTAL | finalize IRA report, site closure including assessment of |
| 34 | Road Landfill (H) | , | | | | | | | | 00 | 60 | residual asbestos |
| RVAAP- | Load Line 11 (H) | RI/FS | 40 | | | | | | | 40 | | finalize IRA and RI report |
| 44 | Load Line 11 (11) | LTM | -10 | | 449 | 20 | 20 | 20 | 40 | 549 | | 10 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 589 | closure report |
| RVAAP- | Bldg F-15 & F-16 (H) | RI/FS | 51 | 161 | 147 | | | | | 359 | | sampling 2 areas |
| 46 | • | RD | | | | 34 | | | | 34 | | design of RA |
| | | RA | | | | | 420 | 54 | | 474 | | sediment removal 200cy for explosives & metals, closure |
| | | | | | | | | | | | 867 | docs |
| RVAAP- | Central Burn Pits (H) | RI/FS | 284 | 120 | | | | | | 404 | | finalize RI, FS, Eco data gaps 60K |
| 49 | | RD | | | 16 | | | | | 16 | | design of RA |
| | | RA | | | 804 | | | | | 804 | | metals fixation 1,000cy, removal 500cy |
| | | LTM | | | | 552 | 30 | 30 | 90 | 702 | | 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 1,926 | closure report |
| RVAAP- | Dump Along Paris | LTM | 40 | 14 | | | | | | 54 | | 4 wells, quarterly for 2 yrs, semi-annual for 1 yr, annual for |
| 51 | Windham Rd. (H) | | | | | | | | | | 54 | 2 yrs, closure reports |
| RVAAP- | Load Line 4 (M) | RI/FS | 50 | | | | | | | 50 | | finalize FS |
| 11 | Load Line 4 (W) | RD | 30 | 10 | | | | | | 10 | | design of RA |
| | | RA | | 30 | 40 | 20 | | | | 90 | | RA funded in FY03 under FPR= Soil removal ~2,000cy, |
| | | 10.1 | | 50 | 40 | 20 | | | | 50 | | costs shown are in-house for COE |
| | | LTM | | | | | 168 | 20 | 80 | 268 | | 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | 100 | | 00 | 200 | 418 | closure report |
| RVAAP- | Upper & Lower Cobbs | RI/FS | 49 | 204 | | | | | | 253 | | Finalize RI. HH & Eco risk Eco sampling to be done as part |
| 29 | Ponds (M) | , . • | | _0. | | | | | | | | of facility-wide surface water study. |
| | () | LTM | | | 609 | 30 | 30 | 30 | 60 | 759 | | 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 1,012 | closure report |
| RVAAP- | 40 MM Firing Range | RI/FS | 20 | | | | 284 | 30 | | 334 | 334 | sampling with UXO precautions |
| 32 | (M) | | | | | | | | | | | 3 |
| RVAAP- | Load Line 6 Fuze and | RI/FS | 136 | 40 | 40 | 100 | | | | 316 | | RI/FS including GW, Eco data gaps 60K |
| 33 | Booster (M) | RD | | | | | 17 | | | 17 | | design of RA |
| | () | RA | | | | | | 747 | | 747 | | soil removal 2,000cy |
| | | LTM | | | | | | 569 | 200 | 769 | | 10 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 1,849 | closure report |
| RVAAP- | Pistol Range (M) | RD | 22 | | | | | | | 22 | | design of RA |
| 36 | | RA | | 388 | | | | | | 388 | | remove top ~foot of soil (~450cy), screen, fix, backfill, reveg |
| | | | | | | | | | | | 410 | |
| RVAAP- | NACA Test Area (M) | RI/FS | | 128 | 17 | 332 | | | | 477 | | RI/FS including 12 wells, Risk HH & eco, Eco data gaps |
| 38 | | | | | | | | | | | | 60K |
| | | RD | | | | 24 | | | | 24 | | design of RA |
| | | RA | | | | | 237 | | | 237 | | soil bio remediation 2 acres |
| | | LTM | | | | | | 414 | 150 | 564 | 1,302 | 12 wells, starting at quarterly, closure report |

| | | | | | | | | • | | , | | • |
|---------------|----------------------|--------------|------|------|------|------|------|-----|-------|-------|--------------|--|
| DSERTS | | | | | | | | | | PHASE | | |
| # | SITE TITLE (RRSE) | PHASE | FY04 | FY05 | FY06 | FY07 | FY08 | | FY10+ | TOTAL | TOTAL | DESCRIPTION OF WORK |
| RVAAP- | Load Line 5 Fuze and | RI/FS | | | | 997 | 40 | 120 | | 1,157 | | RI/FS including GW, Eco data gaps 60K |
| 39 | Booster (M) | RD | | | | | | | 8 | 8 | | design of RA |
| | | RA | | | | | | | 258 | 258 | | soil/sump removal 20cy |
| | | LTM | | | | | | | 369 | 369 | | 6 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 1,792 | closure report |
| RVAAP- | Load Line 8 Fuze and | RI/FS | | | 502 | 495 | 40 | 120 | | 1,157 | | RI/FS including GW, Eco data gaps 60K |
| 41 | Booster (M) | RD | | | | | | | 8 | 8 | | design of RA |
| | | RA | | | | | | | 258 | 258 | | soil/sump removal 20cy |
| | | LTM | | | | | | | 369 | 369 | | 6 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 1,792 | closure report |
| RVAAP- | Load Line 9 Fuze and | RI/FS | 118 | 83 | | | | | | 201 | | RI/FS including GW, Eco data gaps 60K |
| 42 | Booster (M) | RD | | | 8 | | | | | 8 | | design of RA |
| | , , | RA | | | | 258 | | | | 258 | | soil/sump removal 20cy |
| | | LTM | | | | | 197 | 20 | 80 | 297 | | 6 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 764 | closure report |
| RVAAP- | Load Line 10 | RI/FS | | | | 499 | 610 | 120 | | 1,229 | | RI/FS including GW, Eco data gaps 60K |
| 43 | Percussion Element | RD | | | | | | | 8 | 8 | | design of RA |
| | (M) | RA | | | | | | | 258 | 258 | | soil/sump removal 20cy |
| | | LTM | | | | | | | 297 | 297 | | 6 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 1,792 | closure report |
| RVAAP- | Anchor Test Area (M) | RI/FS | | | | | | 200 | 84 | 284 | | Phase II RI |
| 48 | | LTM | | | | | | | 1,137 | 1,137 | 1,421 | 4 wells, semi-annual |
| RVAAP- | Atlas Scrap Yard (M) | RI/FS | | | | | | 492 | 150 | 642 | | UXO support - 100 soil locations, ~6-8 wells, ~8 sediment, |
| 50 | | | | | | | | | | | | 2 surface water, Risk, eco, Eco data gaps 60K |
| | | | | | | | | | | | | - , |
| | | RD | | | | | | | 80 | 80 | | design of RA |
| | | RA | | | | | | | 1,156 | 1,156 | | debis and soil removal |
| | | LTM | | | | | | | 360 | 360 | | 8 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 2,238 | closure report |
| RVAAP- | C Block Quarry (L) | RI/FS | | | | | | | 965 | 965 | | RI/FS, DD |
| 06 | C Block Quality (L) | RD | | | | | | | 33 | 33 | | design of RA |
| 00 | | RA | | | | | | | 1,893 | 1,893 | | Soil removal ~5,000cy |
| | | LTM | | | | | | | 454 | 454 | | 4 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | LIIVI | | | | | | | 454 | 404 | 3,345 | closure report |
| RVAAP- | Bldg. 1200 (L) | RI/FS | | | | | | | 686 | 686 | 3,343 | complete a RI/FS |
| 13 | Diug. 1200 (L) | RD | | | | | | | 5 | 5 | | design of RA |
| 13 | | RA | | | | | | | 213 | 213 | | 200cy soil removal |
| | | LTM | | | | | | | 400 | 400 | | 4 wells, quarterly for 2 yrs, semi-annual for 1 yr, annual for |
| | | | | | | | | | 400 | 400 | 1 204 | 2 yrs, closure reports |
| L | | | | | | | | | | | 1,304 | z yrs, dosure reports |

| DSERTS | | | | | | | | | | PHASE | SITE | |
|-----------------------------------|---|--------------|---------|--------|----------|------|------|------|-------|-----------------|--------------|--|
| # | SITE TITLE (RRSE) | PHASE | FY04 | FY05 | FY06 | FY07 | FY08 | FY09 | FY10+ | TOTAL | TOTAL | DESCRIPTION OF WORK |
| RVAAP- | Landfill North of | RI/FS | | | | | | | 611 | 611 | | Additional RI/FS including 4 wells |
| 19 | Winklepeck Burning | RD | | | | | | | 41 | 41 | | design of RA |
| | Ground (L) | RA | | | | | | | 988 | 988 | | Limit soil cover (2 ft) on ~2.5 acres |
| | | RA(O) | | | | | | | 66 | 66 | | cap maintenance |
| | | LTM | | | | | | | 210 | 210 | | 4 wells, quarterly for 2 yrs, semi-annual for 1 yr, annual for |
| | | | | | | | | | | | 1,916 | 2 yrs, closure reports |
| | <u> </u> | RI/FS | 162 | | | | | | | 162 | | install 4 wells |
| | Site (L) | | | | | | | | | | 162 | |
| RVAAP- | Load Line 7 Fuze and | RI/FS | | | | | | | 1,157 | 1,157 | | RI/FS including GW, Eco data gaps 60K |
| 40 | Booster (L) | RD | | | | | | | 8 | 8 | | design of RA |
| | | RA | | | | | | | 258 | 258 | | soil/sump removal 20cy |
| | | LTM | | | | | | | 369 | 369 | | 6 wells, quarterly for 2 yrs, 1 yr semi-annual, 2 yrs annual, |
| | | | | | | | | | | | 1,792 | closure report |
| RVAAP- | Wet Storage Area (L) | RI/FS | | | | | | | 359 | 359 | | complete RI, site closure |
| 45 | | RA | | | | | | | 120 | 120 | | soil removal ~50cy |
| FY | TOTALS IN THOUSAN | | | | | | | | | 36,718 | 36,718 | |
| | POM \$s 2,381 2,763 5,512 4,842 3,343 3,828 | | | | | | | | | | | |
| Difference 386 130 85 203 572 211 | | | | | | | | | | | 36,718 | |
| Estimates | have been based on th | ne RACEI | R syste | m unle | ss noted | d. | | | | , in the second | | |

COMMUNITY INVOLVEMENT

The RVAAP Restoration Advisory Board (RAB) was established in 1996 and has 25 members consisting of 23 community members and 2 non-community members. The community members include a township appointee from each of the surrounding 6 townships, one representative appointed by the Trumbull County Commissioners, a representative appointed by the Portage County Commissioners, and 15 members chosen from the general public. One of the community members is elected as a community co-chair by majority vote. The two non-community members include a representative of the Ohio EPA and an Army installation co-chair appointed by the installation. A RAB operating procedure was adopted by all members on February 19, 1997. A copy can be found in the RVAAP technical library, as well as two public repositories.

The RVAAP RAB generally meets every two to three months depending on the need for relevant issues to be addressed. All meetings are open to the public and are rotated among public places within the townships around the installation. Current topics are addressed at the meetings and a speaker is generally featured. There have been presentations by the Ohio Department of Health addressing health issues related to the cleanup; by the contractors that are performing remediation work; by WES on the explosive uptake by vegitation; Corps of Engineers describing newly identified contaminated sites; and the Army Center for Health Promotion and Preventative Medicine to explain the rating of AOCs for funding and the process of performing ecological and human health risk assessments. The minutes of all RAB meetings are recorded. All meetings are announced in the local media. A tour for RAB members and the media has been conducted each summer to view AOCs where work is underway. The latest tour was held on July 27, 2002. Regular RAB meetings were held during the past year covering such topics as Guaranteed Fixed Price Remediation (now called PBC) at LLs 1-4, progress of the remedial investigations at Open Demo Area #2 and Fuze and Booster Quarry Ponds/Landfill and thermal decontamination at excess production buildings. A summer tour was not held in 2003 due to the lack of interest.

All IRP records are made available to the RAB members and any other interested parties through the two local libraries. A web site where all IRP and other RVAAP documents will be available is currently under development. RVAAP publishes the semiannual Community Access Newsletters to keep the public up to date on all IRP and other environmental work at RVAAP. The RAB received \$25,000 for technical assistance for public participation (TAPP) (technical review) in April 1999. They recently received a second TAPP grant of \$25,000. This funding was used to review the Ecological Field Truthing report for Winklepeck Burning Grounds. The review of the report by the TAPP provider and the RAB were favorable.

In 2003, a Community Relation Plan was written to facilitate communication, identify issues of concern and serve as a guide for public involement goals and objectives. The plan outlines the many ways that Ravanna AAP involves the community in the restoration activities, including through the RAB, site tours and issuance of fact sheets and newletters.
